


[illegible]

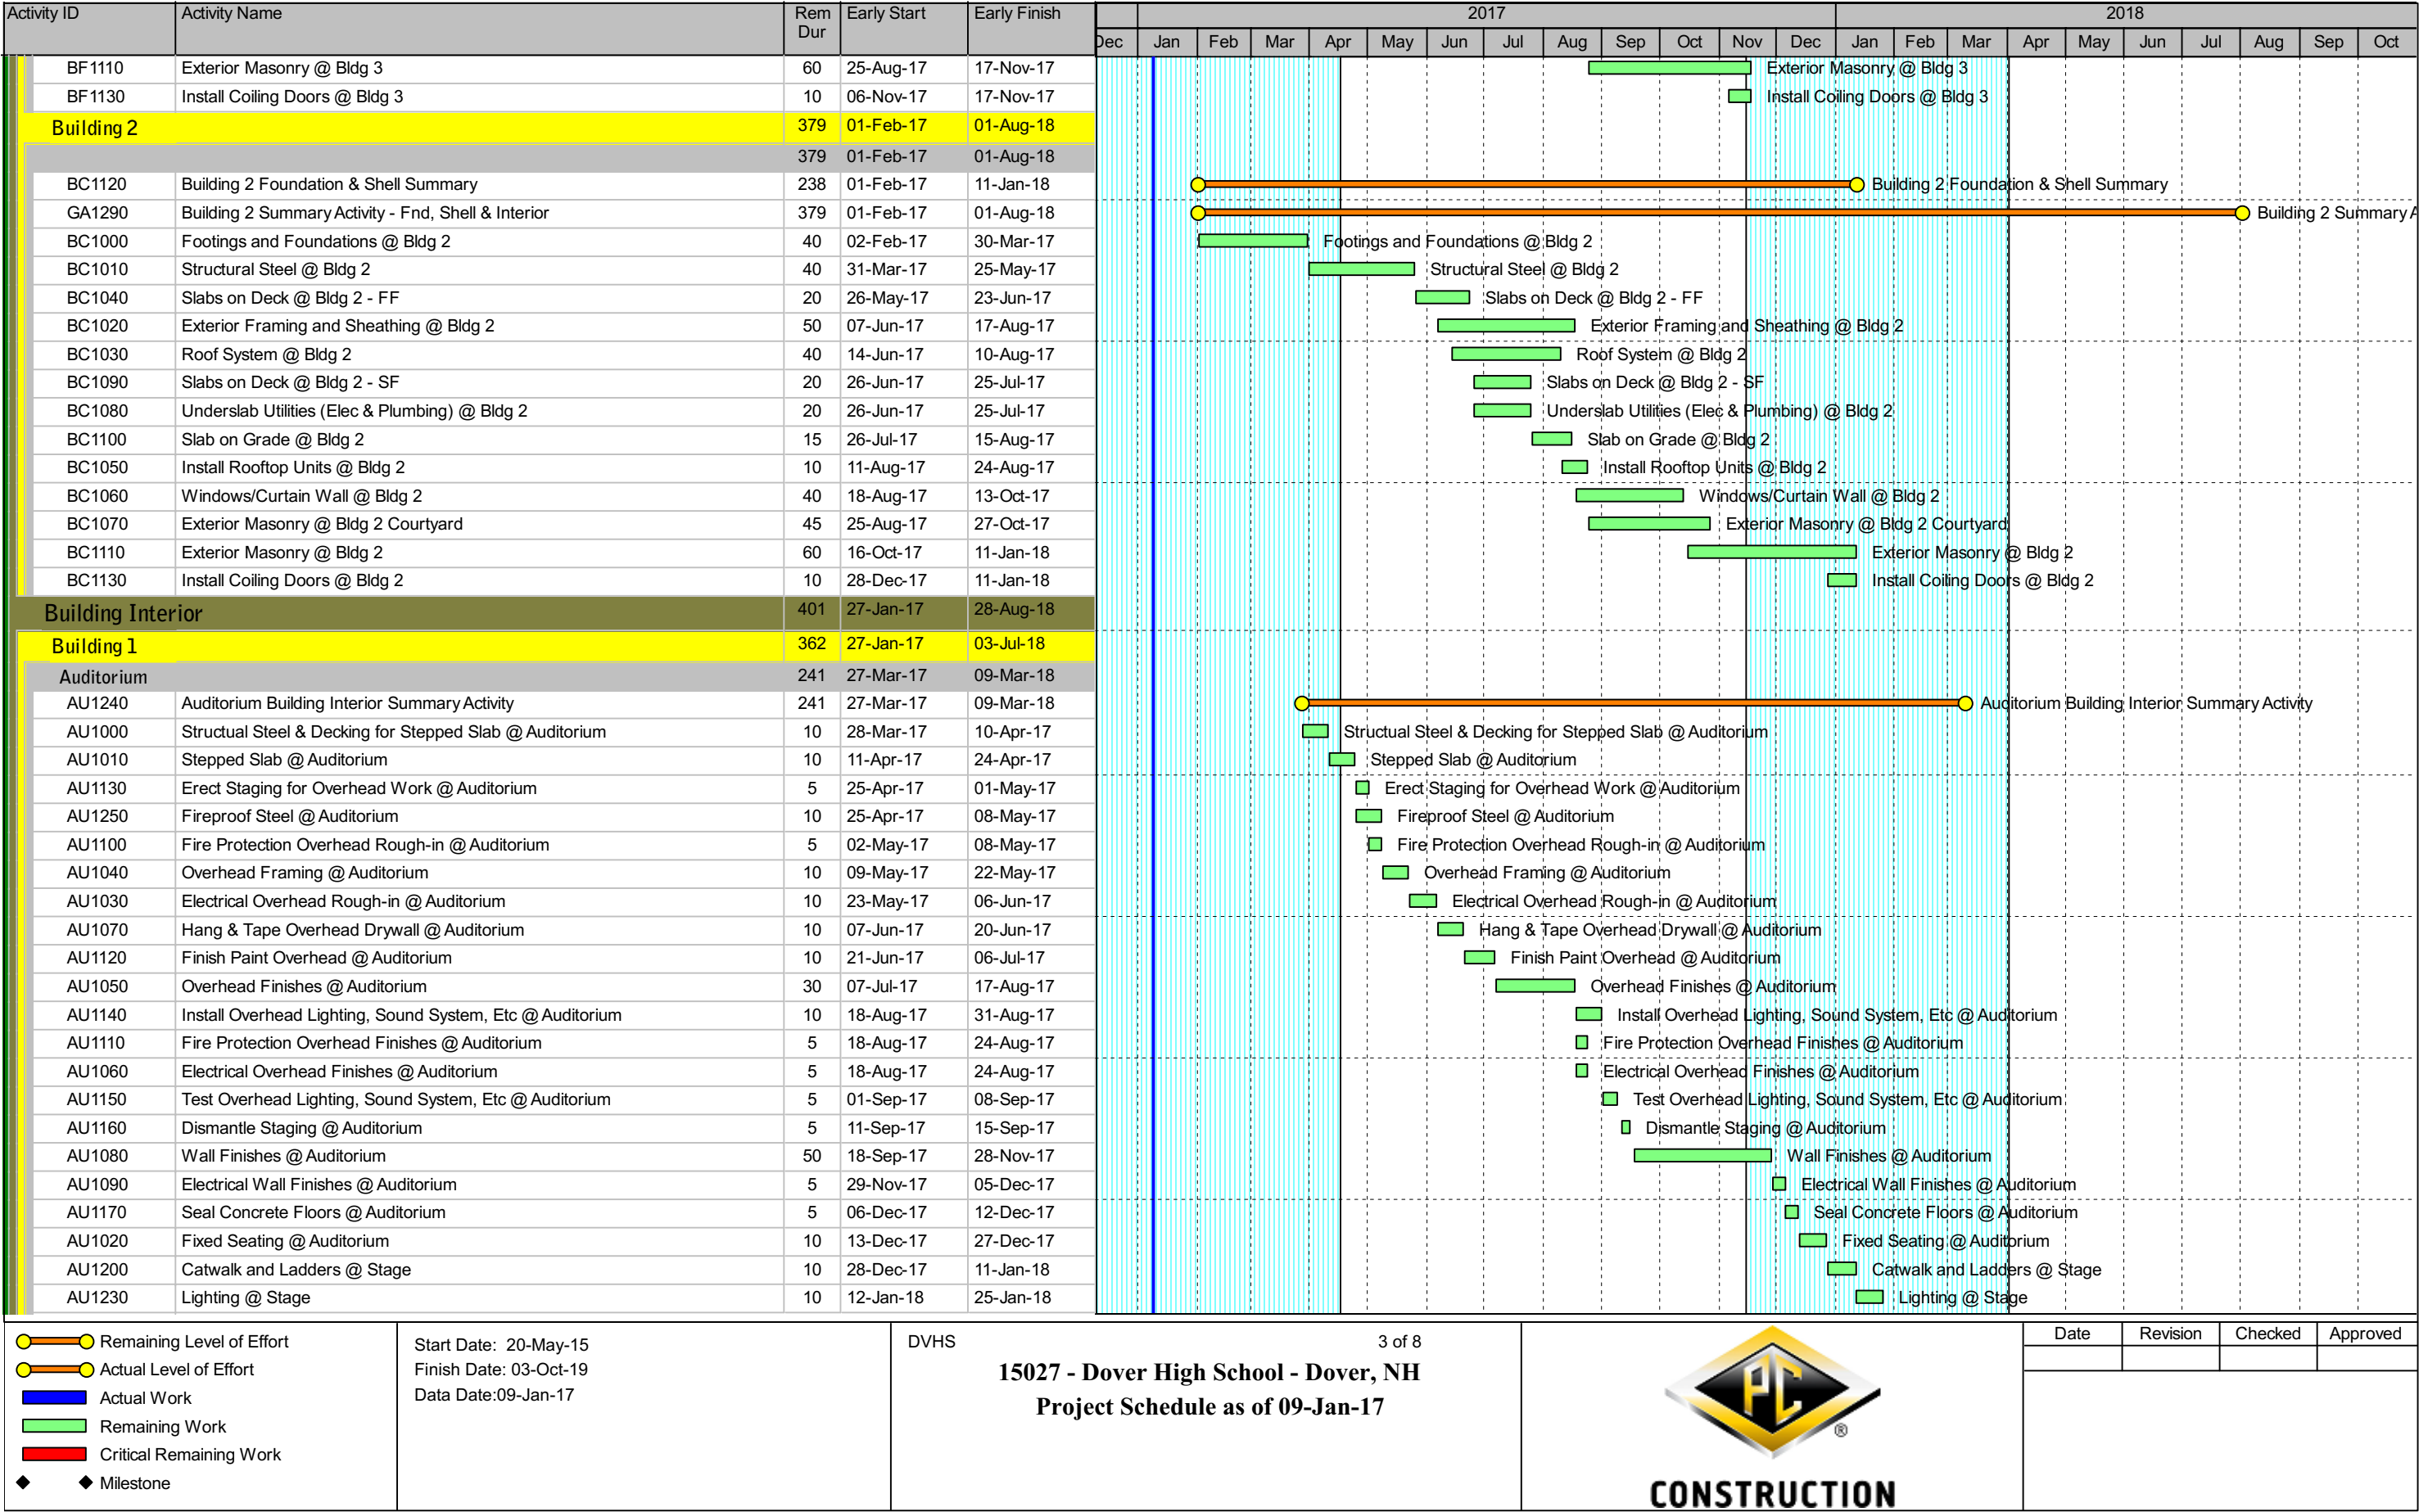

Activity ID	Activity Name	Rem Dur	Early Start	Early Finish	2017													2018									
					Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
AU1210	Rigging and Curtains @ Stage	10	26-Jan-18	08-Feb-18																							
AU1220	Flooring @ Stage	10	09-Feb-18	23-Feb-18																							
AU1180	Carpeting @ Auditorium	5	26-Feb-18	02-Mar-18																							
AU1190	Final Clean @ Auditorium	5	05-Mar-18	09-Mar-18																							
Ground Floor		221	27-Mar-17	08-Feb-18																							
GA1230	Building 1 Ground Floor Summary Activity	221	27-Mar-17	08-Feb-18																							
GA1220	Entire Ground Floor Building Interior Summary Activity	221	27-Mar-17	08-Feb-18																							
GA1210	Masonry Elevator Shaft @ Bldg 1 - GF	15	28-Mar-17	17-Apr-17																							
GA1000	Interior Framing @ Bldg 1 - GF	25	28-Mar-17	01-May-17																							
GA1030	Plumbing Above Ceiling Rough-in @ Bldg 1 - GF	30	18-Apr-17	30-May-17																							
GA1060	Plumbing In Wall Rough-in @ Bldg 1 - GF	30	02-May-17	13-Jun-17																							
GA1050	Electrical In Wall Rough-in @ Bldg 1 - GF	30	02-May-17	13-Jun-17																							
GA1040	Mechanical In Wall Rough-in @ Bldg 1- GF	30	02-May-17	13-Jun-17																							
GC1240	Electrical Room Fit-up @ Bldg 1 - GF	30	02-May-17	13-Jun-17																							
GC1250	Mechanical Room Fit-up @ Bldg 1 - GF	40	02-May-17	27-Jun-17																							
GA1020	Electrical Above Ceiling Rough-in @ Bldg 1 - GF	30	16-May-17	27-Jun-17																							
GA1010	Mechanical Above Ceiling Rough-in @ Bldg 1 - GF	30	31-May-17	13-Jul-17																							
GA1200	Elevator Installation @ Bldg 1 - GF	25	14-Jun-17	20-Jul-17																							
GA1070	Hang & Tape Drywall @ Bldg 1 - GF	25	14-Jul-17	17-Aug-17																							
GA1090	Ceramic Wall Tile @ Bldg 1 - GF	20	04-Aug-17	31-Aug-17																							
GA1080	Prime & Paint @ Bldg 1 - GF	20	18-Aug-17	15-Sep-17																							
GA1100	Ceiling Grid @ Bldg 1 - GF	15	18-Sep-17	06-Oct-17																							
GA1130	Electrical Finishes @ Bldg 1 - GF	15	09-Oct-17	27-Oct-17																							
GA1120	Mechanical Finishes @ Bldg 1 - GF	15	09-Oct-17	27-Oct-17																							
GA1250	Sprinkler Heads @ Bldg 1 - GF	5	09-Oct-17	13-Oct-17																							
GA1300	Install Wood Gym Flooring @ Bldg 1 - GF	15	16-Oct-17	03-Nov-17																							
GA1320	Install Resilient Gym Flooring @ Bldg 1 - GF	10	16-Oct-17	27-Oct-17																							
GA1260	Drop Ceiling Tiles @ Bldg 1 - GF	5	30-Oct-17	03-Nov-17																							
GA1110	Flooring @ Bldg 1 - GF	20	06-Nov-17	05-Dec-17																							
GA1310	Final Paint Wood Gym Flooring @ Bldg 1 - GF	5	06-Nov-17	10-Nov-17																							
GA1140	Doors & Hardware @ Bldg 1 - GF	20	13-Nov-17	12-Dec-17																							
GA1330	Install Gym Bleachers @ Bldg 1 - GF	10	13-Nov-17	28-Nov-17																							
GA1150	Finish Carpentry (Casework) @ Bldg 1 - GF	25	20-Nov-17	27-Dec-17																							
GA1160	Plumbing Finishes @ Bldg 1 - GF	15	20-Dec-17	11-Jan-18																							
GA1170	Final Paint @ Bldg 1 - GF	10	12-Jan-18	25-Jan-18																							
GA1180	Install Specialties @ Bldg 1 - GF	5	26-Jan-18	01-Feb-18																							
GA1190	Final Clean @ Bldg 1 - GF	5	02-Feb-18	08-Feb-18																							
First Floor		335	27-Jan-17	24-May-18																							
AA1210	Building 1 First Floor Summary Activity	276	27-Jan-17	02-Mar-18																							
AA1200	Entire First Floor Building Interior Summary Activity	335	27-Jan-17	24-May-18																							
AA1000	Interior Framing @ Bldg 1 - FF	25	30-Jan-17	06-Mar-17																							
AA1020	Electrical Above Ceiling Rough-in @ Bldg 1 - FF	30	07-Mar-17	17-Apr-17																							
AA1010	Mechanical Above Ceiling Rough-in @ Bldg 1 - FF	30	07-Mar-17	17-Apr-17																							
AA1030	Plumbing Above Ceiling Rough-in @ Bldg 1 - FF	30	14-Mar-17	24-Apr-17																							

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Start Date: 20-May-15

Finish Date: 03-Oct-19

Data Date:09-Jan-17

DVHS

4 of 8

15027 - Dover High School - Dover, NH

Project Schedule as of 09-Jan-17

PC


CONSTRUCTION

Date

Revision

Checked

Approved

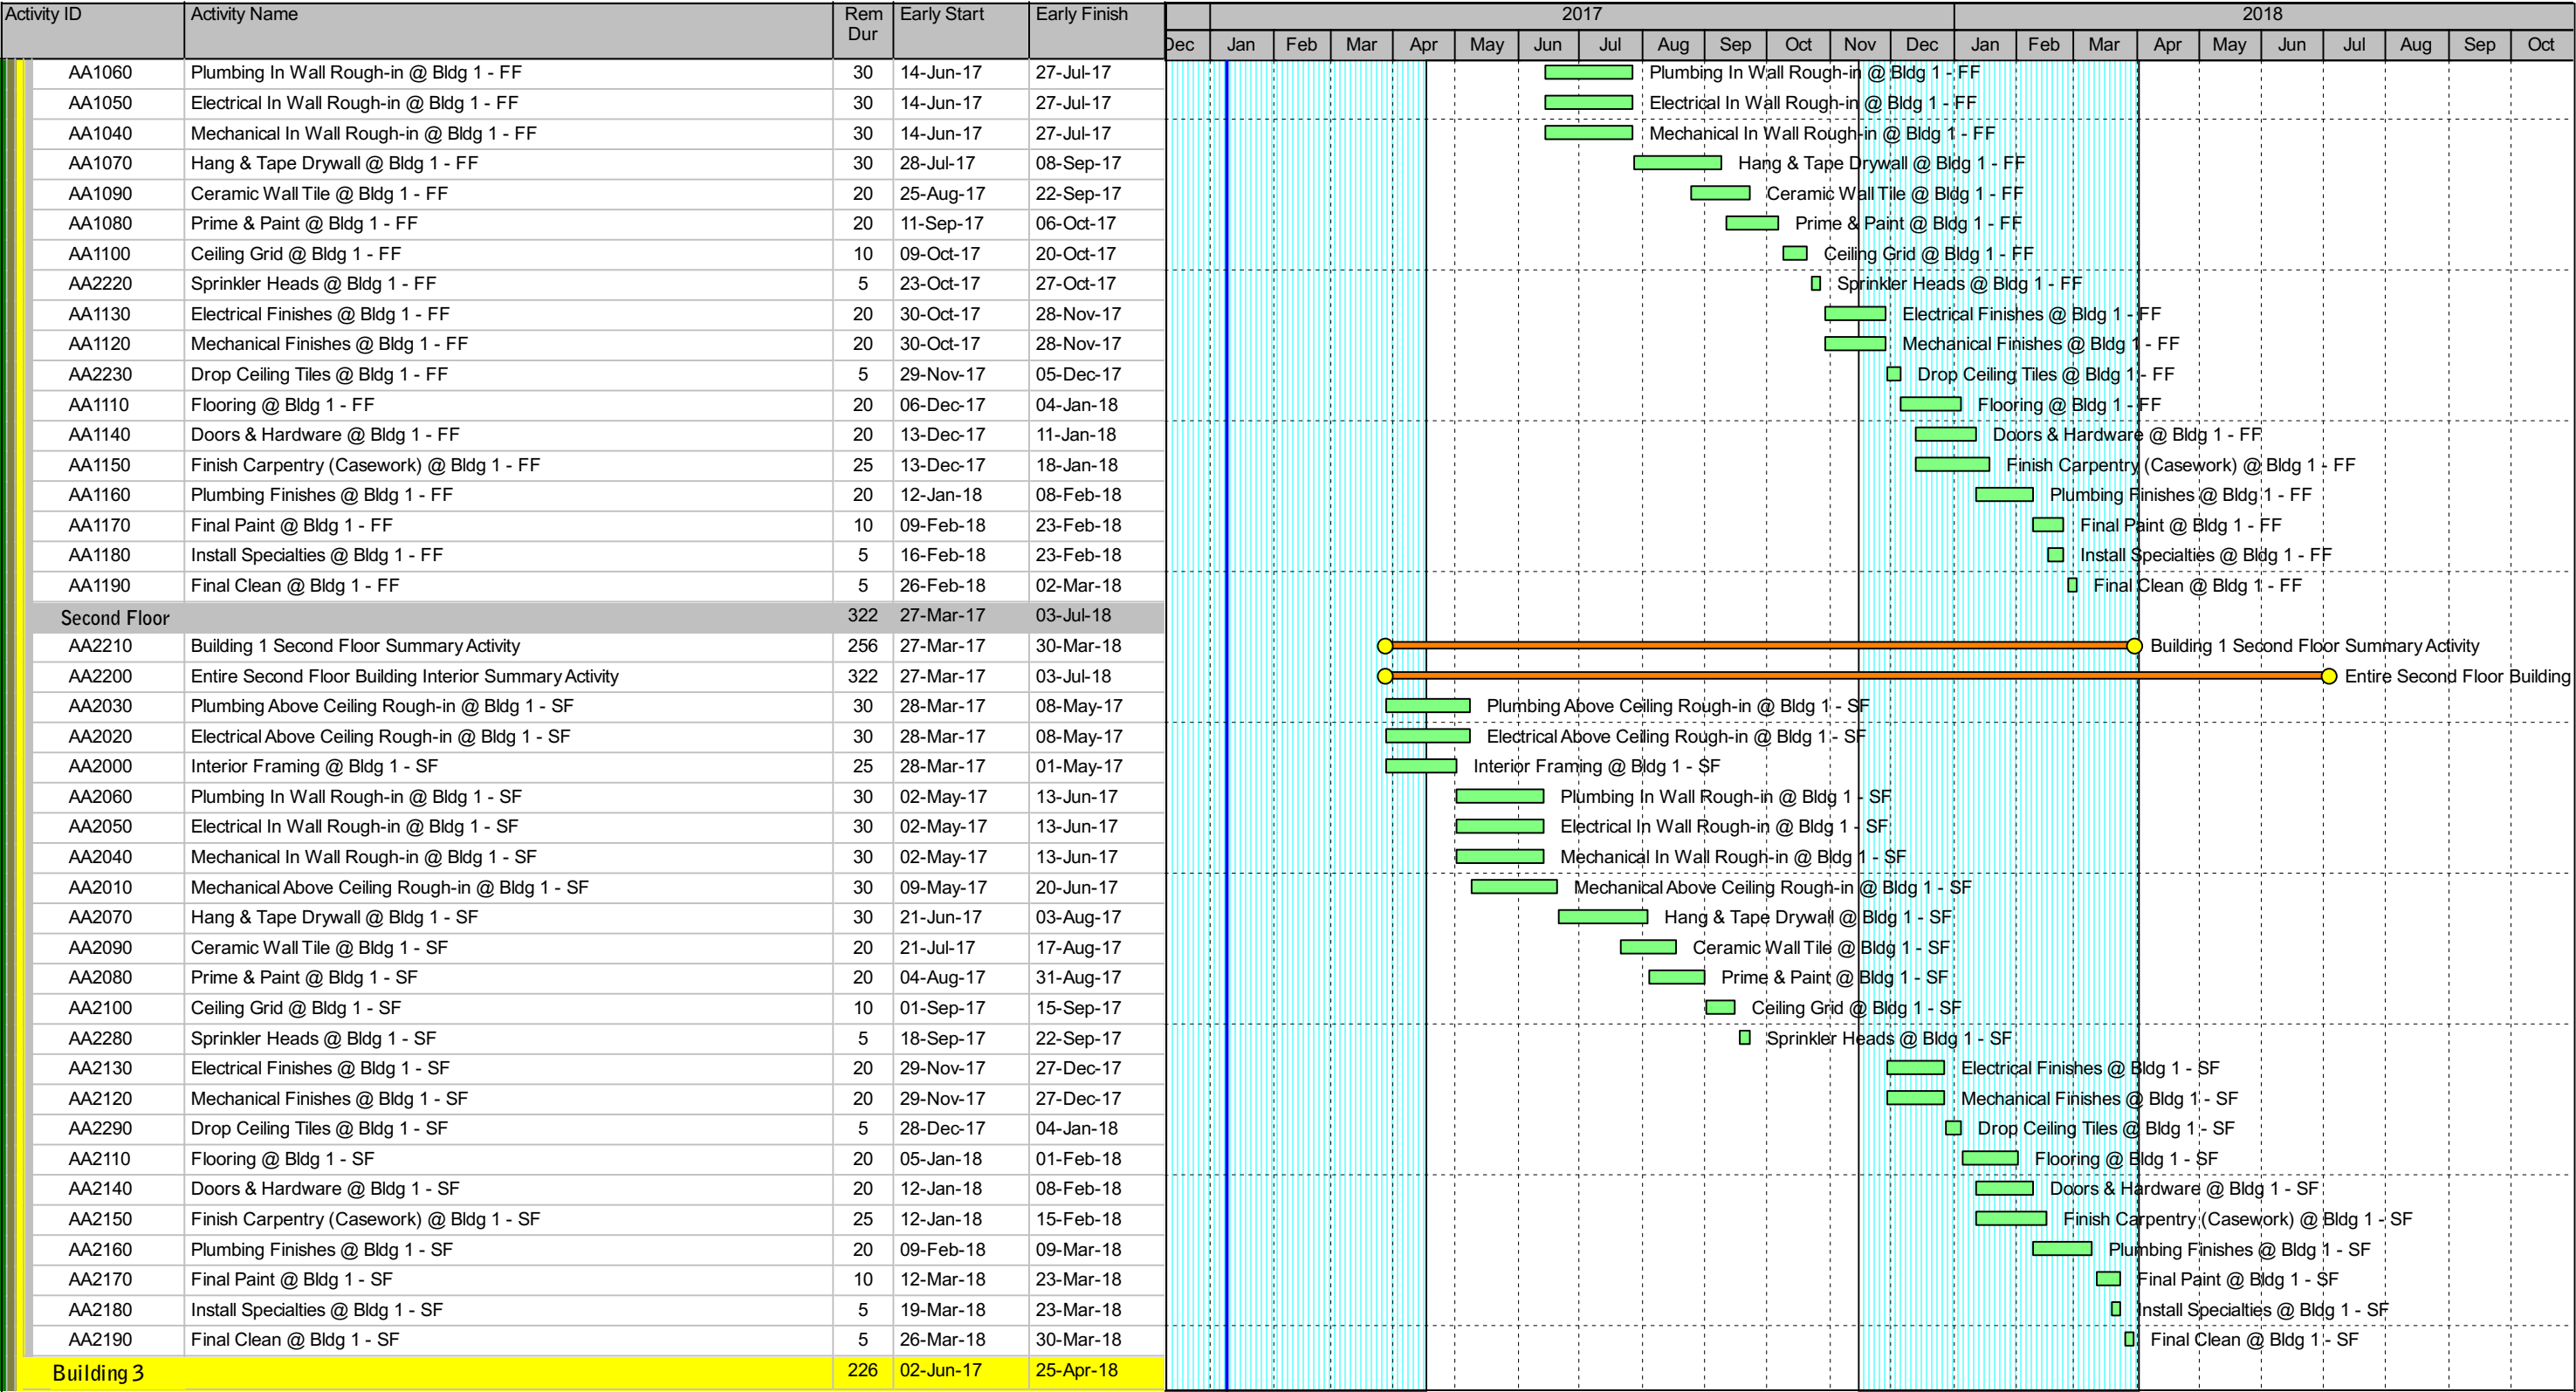

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Start Date: 20-May-15

Finish Date: 03-Oct-19

Data Date:09-Jan-17

DVHS

5 of 8

15027 - Dover High School - Dover, NH

Project Schedule as of 09-Jan-17

PC

CONSTRUCTION

Date	Revision	Checked	Approved

Activity ID	Activity Name	Rem Dur	Early Start	Early Finish	2017													2018															
					Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct						
First Floor		196	02-Jun-17	14-Mar-18																													
AF1200	Building 3 First Floor Summary Activity	196	02-Jun-17	14-Mar-18	Building 3 First Floor Summary Activity																												
AE1200	Masonry Elevator Shaft @ Bldg 3 - FF	10	05-Jun-17	16-Jun-17	Masonry Elevator Shaft @ Bldg 3 - FF																												
AF1030	Plumbing Above Ceiling Rough-in @ Bldg 3 - FF	30	05-Jun-17	18-Jul-17	Plumbing Above Ceiling Rough-in @ Bldg 3 - FF																												
AF1020	Electrical Above Ceiling Rough-in @ Bldg 3 - FF	30	05-Jun-17	18-Jul-17	Electrical Above Ceiling Rough-in @ Bldg 3 - FF																												
AF1010	Mechanical Above Ceiling Rough-in @ Bldg 3 - FF	30	05-Jun-17	18-Jul-17	Mechanical Above Ceiling Rough-in @ Bldg 3 - FF																												
AF1000	Interior Framing @ Bldg 3 - FF	30	05-Jun-17	18-Jul-17	Interior Framing @ Bldg 3 - FF																												
AE1230	Electrical Room Fit-up @ Bldg 3 - FF	10	19-Jul-17	01-Aug-17	Electrical Room Fit-up @ Bldg 3 - FF																												
AF1060	Plumbing In Wall Rough-in @ Bldg 3 - FF	30	19-Jul-17	29-Aug-17	Plumbing In Wall Rough-in @ Bldg 3 - FF																												
AF1050	Electrical In Wall Rough-in @ Bldg 3 - FF	30	19-Jul-17	29-Aug-17	Electrical In Wall Rough-in @ Bldg 3 - FF																												
AF1040	Mechanical In Wall Rough-in @ Bldg 3 - FF	30	19-Jul-17	29-Aug-17	Mechanical In Wall Rough-in @ Bldg 3 - FF																												
AE1210	Elevator Installation @ Bldg 3 - FF	20	02-Aug-17	29-Aug-17	Elevator Installation @ Bldg 3 - FF																												
AF1070	Hang & Tape Drywall @ Bldg 3 - FF	30	30-Aug-17	11-Oct-17	Hang & Tape Drywall @ Bldg 3 - FF																												
AF1090	Ceramic Wall Tile @ Bldg 3 - FF	20	28-Sep-17	25-Oct-17	Ceramic Wall Tile @ Bldg 3 - FF																												
AF1080	Prime & Paint @ Bldg 3 - FF	20	12-Oct-17	08-Nov-17	Prime & Paint @ Bldg 3 - FF																												
AF1100	Ceiling Grid @ Bldg 3 - FF	10	09-Nov-17	22-Nov-17	Ceiling Grid @ Bldg 3 - FF																												
AF1130	Electrical Finishes @ Bldg 3 - FF	20	27-Nov-17	22-Dec-17	Electrical Finishes @ Bldg 3 - FF																												
AF1120	Mechanical Finishes @ Bldg 3 - FF	20	27-Nov-17	22-Dec-17	Mechanical Finishes @ Bldg 3 - FF																												
AA2240	Sprinkler Heads @ Bldg 3 - FF	5	27-Nov-17	01-Dec-17	Sprinkler Heads @ Bldg 3 - FF																												
AA2250	Drop Ceiling Tiles @ Bldg 3 - FF	5	26-Dec-17	02-Jan-18	Drop Ceiling Tiles @ Bldg 3 - FF																												
AF1110	Flooring @ Bldg 3 - FF	20	03-Jan-18	30-Jan-18	Flooring @ Bldg 3 - FF																												
AF1140	Doors & Hardware @ Bldg 3 - FF	20	10-Jan-18	06-Feb-18	Doors & Hardware @ Bldg 3 - FF																												
AF1150	Finish Carpentry (Casework) @ Bldg 3 - FF	25	10-Jan-18	13-Feb-18	Finish Carpentry (Casework) @ Bldg 3 - FF																												
AF1160	Plumbing Finishes @ Bldg 3 - FF	20	24-Jan-18	21-Feb-18	Plumbing Finishes @ Bldg 3 - FF																												
AF1170	Final Paint @ Bldg 3 - FF	10	22-Feb-18	07-Mar-18	Final Paint @ Bldg 3 - FF																												
AF1180	Install Specialties @ Bldg 3 - FF	5	01-Mar-18	07-Mar-18	Install Specialties @ Bldg 3 - FF																												
AF1190	Final Clean @ Bldg 3 - FF	5	08-Mar-18	14-Mar-18	Final Clean @ Bldg 3 - FF																												
Second Floor		200	12-Jul-17	25-Apr-18																													
AF2200	Building 3 Second Floor Summary Activity	200	12-Jul-17	25-Apr-18	Building 3 Second Floor Summary Activity																												
AF2020	Plumbing Above Ceiling Rough-in @ Bldg 3 - SF	30	13-Jul-17	23-Aug-17	Plumbing Above Ceiling Rough-in @ Bldg 3 - SF																												
AF2010	Electrical Above Ceiling Rough-in @ Bldg 3 - SF	30	13-Jul-17	23-Aug-17	Electrical Above Ceiling Rough-in @ Bldg 3 - SF																												
AF2030	Mechanical Above Ceiling Rough-in @ Bldg 3 - SF	30	13-Jul-17	23-Aug-17	Mechanical Above Ceiling Rough-in @ Bldg 3 - SF																												
AF2000	Interior Framing @ Bldg 3- SF	30	13-Jul-17	23-Aug-17	Interior Framing @ Bldg 3- SF																												
AF2050	Electrical In Wall Rough-in @ Bldg 3 - SF	30	24-Aug-17	05-Oct-17	Electrical In Wall Rough-in @ Bldg 3 - SF																												
AF2040	Mechanical In Wall Rough-in @ Bldg 3 - SF	30	24-Aug-17	05-Oct-17	Mechanical In Wall Rough-in @ Bldg 3 - SF																												
AF2060	Plumbing In Wall Rough-in @ Bldg 3 - SF	30	30-Aug-17	11-Oct-17	Plumbing In Wall Rough-in @ Bldg 3 - SF																												
AF2070	Hang & Tape Drywall @ Bldg 3 - SF	30	12-Oct-17	22-Nov-17	Hang & Tape Drywall @ Bldg 3 - SF																												
AF2090	Ceramic Wall Tile @ Bldg 3 - SF	20	09-Nov-17	08-Dec-17	Ceramic Wall Tile @ Bldg 3 - SF																												
AF2080	Prime & Paint @ Bldg 3 - SF	20	27-Nov-17	22-Dec-17	Prime & Paint @ Bldg 3 - SF																												
AF2100	Ceiling Grid @ Bldg 3 - SF	10	26-Dec-17	09-Jan-18	Ceiling Grid @ Bldg 3 - SF																												
AF2130	Electrical Finishes @ Bldg 3 - SF	20	10-Jan-18	06-Feb-18	Electrical Finishes @ Bldg 3 - SF																												
AF2120	Mechanical Finishes @ Bldg 3 - SF	20	10-Jan-18	06-Feb-18	Mechanical Finishes @ Bldg 3 - SF																												
AF2210	Sprinkler Heads @ Bldg 3 - SF	5	10-Jan-18	16-Jan-18	Sprinkler Heads @ Bldg 3 - SF																												
AF2220	Drop Ceiling Tiles @ Bldg 3 - SF	5	07-Feb-18	13-Feb-18	Drop Ceiling Tiles @ Bldg 3 - SF																												

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Start Date: 20-May-15

Finish Date: 03-Oct-19

Data Date:09-Jan-17

DVHS

6 of 8

15027 - Dover High School - Dover, NH

Project Schedule as of 09-Jan-17

PC

CONSTRUCTION

Date

Revision

Checked

Approved

Activity ID	Activity Name	Rem Dur	Early Start	Early Finish	2017													2018									
					Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
AF2110	Flooring @ Bldg 3 - SF	20	14-Feb-18	14-Mar-18																							
AF2140	Doors & Hardware @ Bldg 3 - SF	20	22-Feb-18	21-Mar-18																							
AF2150	Finish Carpentry (Casework) @ Bldg 3 - SF	25	22-Feb-18	28-Mar-18																							
AF2160	Plumbing Finishes @ Bldg 3 - SF	20	08-Mar-18	04-Apr-18																							
AF2170	Final Paint @ Bldg 3 - SF	10	05-Apr-18	18-Apr-18																							
AF2180	Install Specialties @ Bldg 3 - SF	5	12-Apr-18	18-Apr-18																							
AF2190	Final Clean @ Bldg 3 - SF	5	19-Apr-18	25-Apr-18																							
Building 2		223	16-Aug-17	03-Jul-18																							
First Floor		196	16-Aug-17	24-May-18																							
AC1200	Building 2 First Floor Summary Activity	196	16-Aug-17	24-May-18																							
AC1030	Plumbing Above Ceiling Rough-in @ Bldg 2 - FF	30	17-Aug-17	28-Sep-17																							
AC1020	Electrical Above Ceiling Rough-in @ Bldg 2 - FF	30	17-Aug-17	28-Sep-17																							
AC1010	Mechanical Above Ceiling Rough-in @ Bldg 2 - FF	30	17-Aug-17	28-Sep-17																							
AC1000	Interior Framing @ Bldg 2 - FF	30	17-Aug-17	28-Sep-17																							
AC1060	Plumbing In Wall Rough-in @ Bldg 2 - FF	30	29-Sep-17	09-Nov-17																							
AC1050	Electrical In Wall Rough-in @ Bldg 2 - FF	30	29-Sep-17	09-Nov-17																							
AC1040	Mechanical In Wall Rough-in @ Bldg 2 - FF	30	29-Sep-17	09-Nov-17																							
AC1070	Hang & Tape Drywall @ Bldg 2 - FF	30	10-Nov-17	26-Dec-17																							
AC1090	Ceramic Wall Tile @ Bldg 2 - FF	20	12-Dec-17	10-Jan-18																							
AC1080	Prime & Paint @ Bldg 2 - FF	20	27-Dec-17	24-Jan-18																							
AC1100	Ceiling Grid @ Bldg 2 - FF	10	25-Jan-18	07-Feb-18																							
AC1130	Electrical Finishes @ Bldg 2 - FF	20	08-Feb-18	08-Mar-18																							
AC1120	Mechanical Finishes @ Bldg 2 - FF	20	08-Feb-18	08-Mar-18																							
AA2260	Sprinkler Heads @ Bldg 2 - FF	5	08-Feb-18	14-Feb-18																							
AA2270	Drop Ceiling Tiles @ Bldg 2 - FF	5	09-Mar-18	15-Mar-18																							
AC1110	Flooring @ Bldg 2 - FF	20	16-Mar-18	12-Apr-18																							
AC1140	Doors & Hardware @ Bldg 2 - FF	20	23-Mar-18	19-Apr-18																							
AC1150	Finish Carpentry (Casework) @ Bldg 2 - FF	25	23-Mar-18	26-Apr-18																							
AC1160	Plumbing Finishes @ Bldg 2 - FF	20	06-Apr-18	03-May-18																							
AC1170	Final Paint @ Bldg 2 - FF	10	04-May-18	17-May-18																							
AC1180	Install Specialties @ Bldg 2 - FF	5	11-May-18	17-May-18																							
AC1190	Final Clean @ Bldg 2 - FF	5	18-May-18	24-May-18																							
Second Floor		196	25-Sep-17	03-Jul-18																							
AC2200	Building 2 Second Floor Summary Activity	196	25-Sep-17	03-Jul-18																							
AC2030	Plumbing Above Ceiling Rough-in @ Bldg 2 - SF	30	26-Sep-17	06-Nov-17																							
AC2020	Electrical Above Ceiling Rough-in @ Bldg 2 - SF	30	26-Sep-17	06-Nov-17																							
AC2010	Mechanical Above Ceiling Rough-in @ Bldg 2 - SF	30	26-Sep-17	06-Nov-17																							
AC2000	Interior Framing @ Bldg 2 - SF	30	26-Sep-17	06-Nov-17																							
AC2060	Plumbing In Wall Rough-in @ Bldg 2 - SF	30	07-Nov-17	20-Dec-17																							
AC2050	Electrical In Wall Rough-in @ Bldg 2 - SF	30	07-Nov-17	20-Dec-17																							
AC2040	Mechanical In Wall Rough-in @ Bldg 2 - SF	30	07-Nov-17	20-Dec-17																							
AC2070	Hang & Tape Drywall @ Bldg 2 - SF	30	21-Dec-17	02-Feb-18																							
AC2090	Ceramic Wall Tile @ Bldg 2 - SF	20	22-Jan-18	16-Feb-18																							
AC2080	Prime & Paint @ Bldg 2 - SF	20	05-Feb-18	05-Mar-18																							

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Start Date: 20-May-15

Finish Date: 03-Oct-19

Data Date:09-Jan-17

DVHS

7 of 8

15027 - Dover High School - Dover, NH

Project Schedule as of 09-Jan-17

PC

CONSTRUCTION

Date

Revision

Checked

Approved

Activity ID	Activity Name	Rem Dur	Early Start	Early Finish	2017													2018									
					Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
AC2100	Ceiling Grid @ Bldg 2 - SF	10	06-Mar-18	19-Mar-18																							
	Electrical Finishes @ Bldg 2 - SF	20	20-Mar-18	16-Apr-18																							
	Mechanical Finishes @ Bldg 2 - SF	20	20-Mar-18	16-Apr-18																							
	Sprinkler Heads @ Bldg 2 - SF	5	20-Mar-18	26-Mar-18																							
	Drop Ceiling Tiles @ Bldg 2 - SF	5	17-Apr-18	23-Apr-18																							
	Flooring @ Bldg 2 - SF	20	24-Apr-18	21-May-18																							
	Doors & Hardware @ Bldg 2 - SF	20	01-May-18	29-May-18																							
	Finish Carpentry (Casework) @ Bldg 2 - SF	25	01-May-18	05-Jun-18																							
	Plumbing Finishes @ Bldg 2 - SF	20	15-May-18	12-Jun-18																							
	Final Paint @ Bldg 2 - SF	10	13-Jun-18	26-Jun-18																							
	Install Specialties @ Bldg 2 - SF	5	20-Jun-18	26-Jun-18																							
	AC2190	Final Clean @ Bldg 2 - SF	5	27-Jun-18	03-Jul-18																						
Animal Science		111	23-Mar-18	28-Aug-18																							
		111	23-Mar-18	28-Aug-18																							
AS1120	Animal Science Summary Activity	111	23-Mar-18	28-Aug-18																							
AS1000	Foundation Excavation @ Animal Science	5	26-Mar-18	30-Mar-18																							
AS1010	Extend Underground Utilities @ Animal Science	5	02-Apr-18	06-Apr-18																							
AS1020	Footings and Frost Walls @ Animal Science	5	09-Apr-18	13-Apr-18																							
AS1030	Underslab Utilities @ Animal Science	5	16-Apr-18	20-Apr-18																							
AS1040	Slab on Grade @ Animal Science	5	23-Apr-18	27-Apr-18																							
AS1050	Building Assembly (Exterior Envelope) @ Animal Science	20	30-Apr-18	25-May-18																							
AS1060	Interior Framing @ Animal Science	10	29-May-18	11-Jun-18																							
AS1070	MEP Rough-in @ Animal Science	20	05-Jun-18	02-Jul-18																							
AS1080	Interior Finishes @ Animal Science	20	03-Jul-18	31-Jul-18																							
AS1090	Start-up & Commissioning @ Animal Science	10	01-Aug-18	14-Aug-18																							
AS1100	Punchlist & Final Clean @ Animal Science	5	15-Aug-18	21-Aug-18																							
AS1110	Owner FF&E @ Animal Science	5	22-Aug-18	28-Aug-18																							
Abatement, Demolition & Fields		291	25-Jun-18	21-Aug-19																							
		291	25-Jun-18	21-Aug-19																							
		291	25-Jun-18	21-Aug-19																							
		291	25-Jun-18	21-Aug-19																							
AU2060	Phase II Existing Building Abate & Demo	160	25-Jun-18	13-Feb-19																							
AU2070	Phase II Parking Lots, Fields & Courts	90	15-Apr-19	21-Aug-19																							

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆

 Milestone

Start Date: 20-May-15

Finish Date: 03-Oct-19

Data Date:09-Jan-17

DVHS

8 of 8

15027 - Dover High School - Dover, NH

Project Schedule as of 09-Jan-17



Date	Revision	Checked	Approved
