



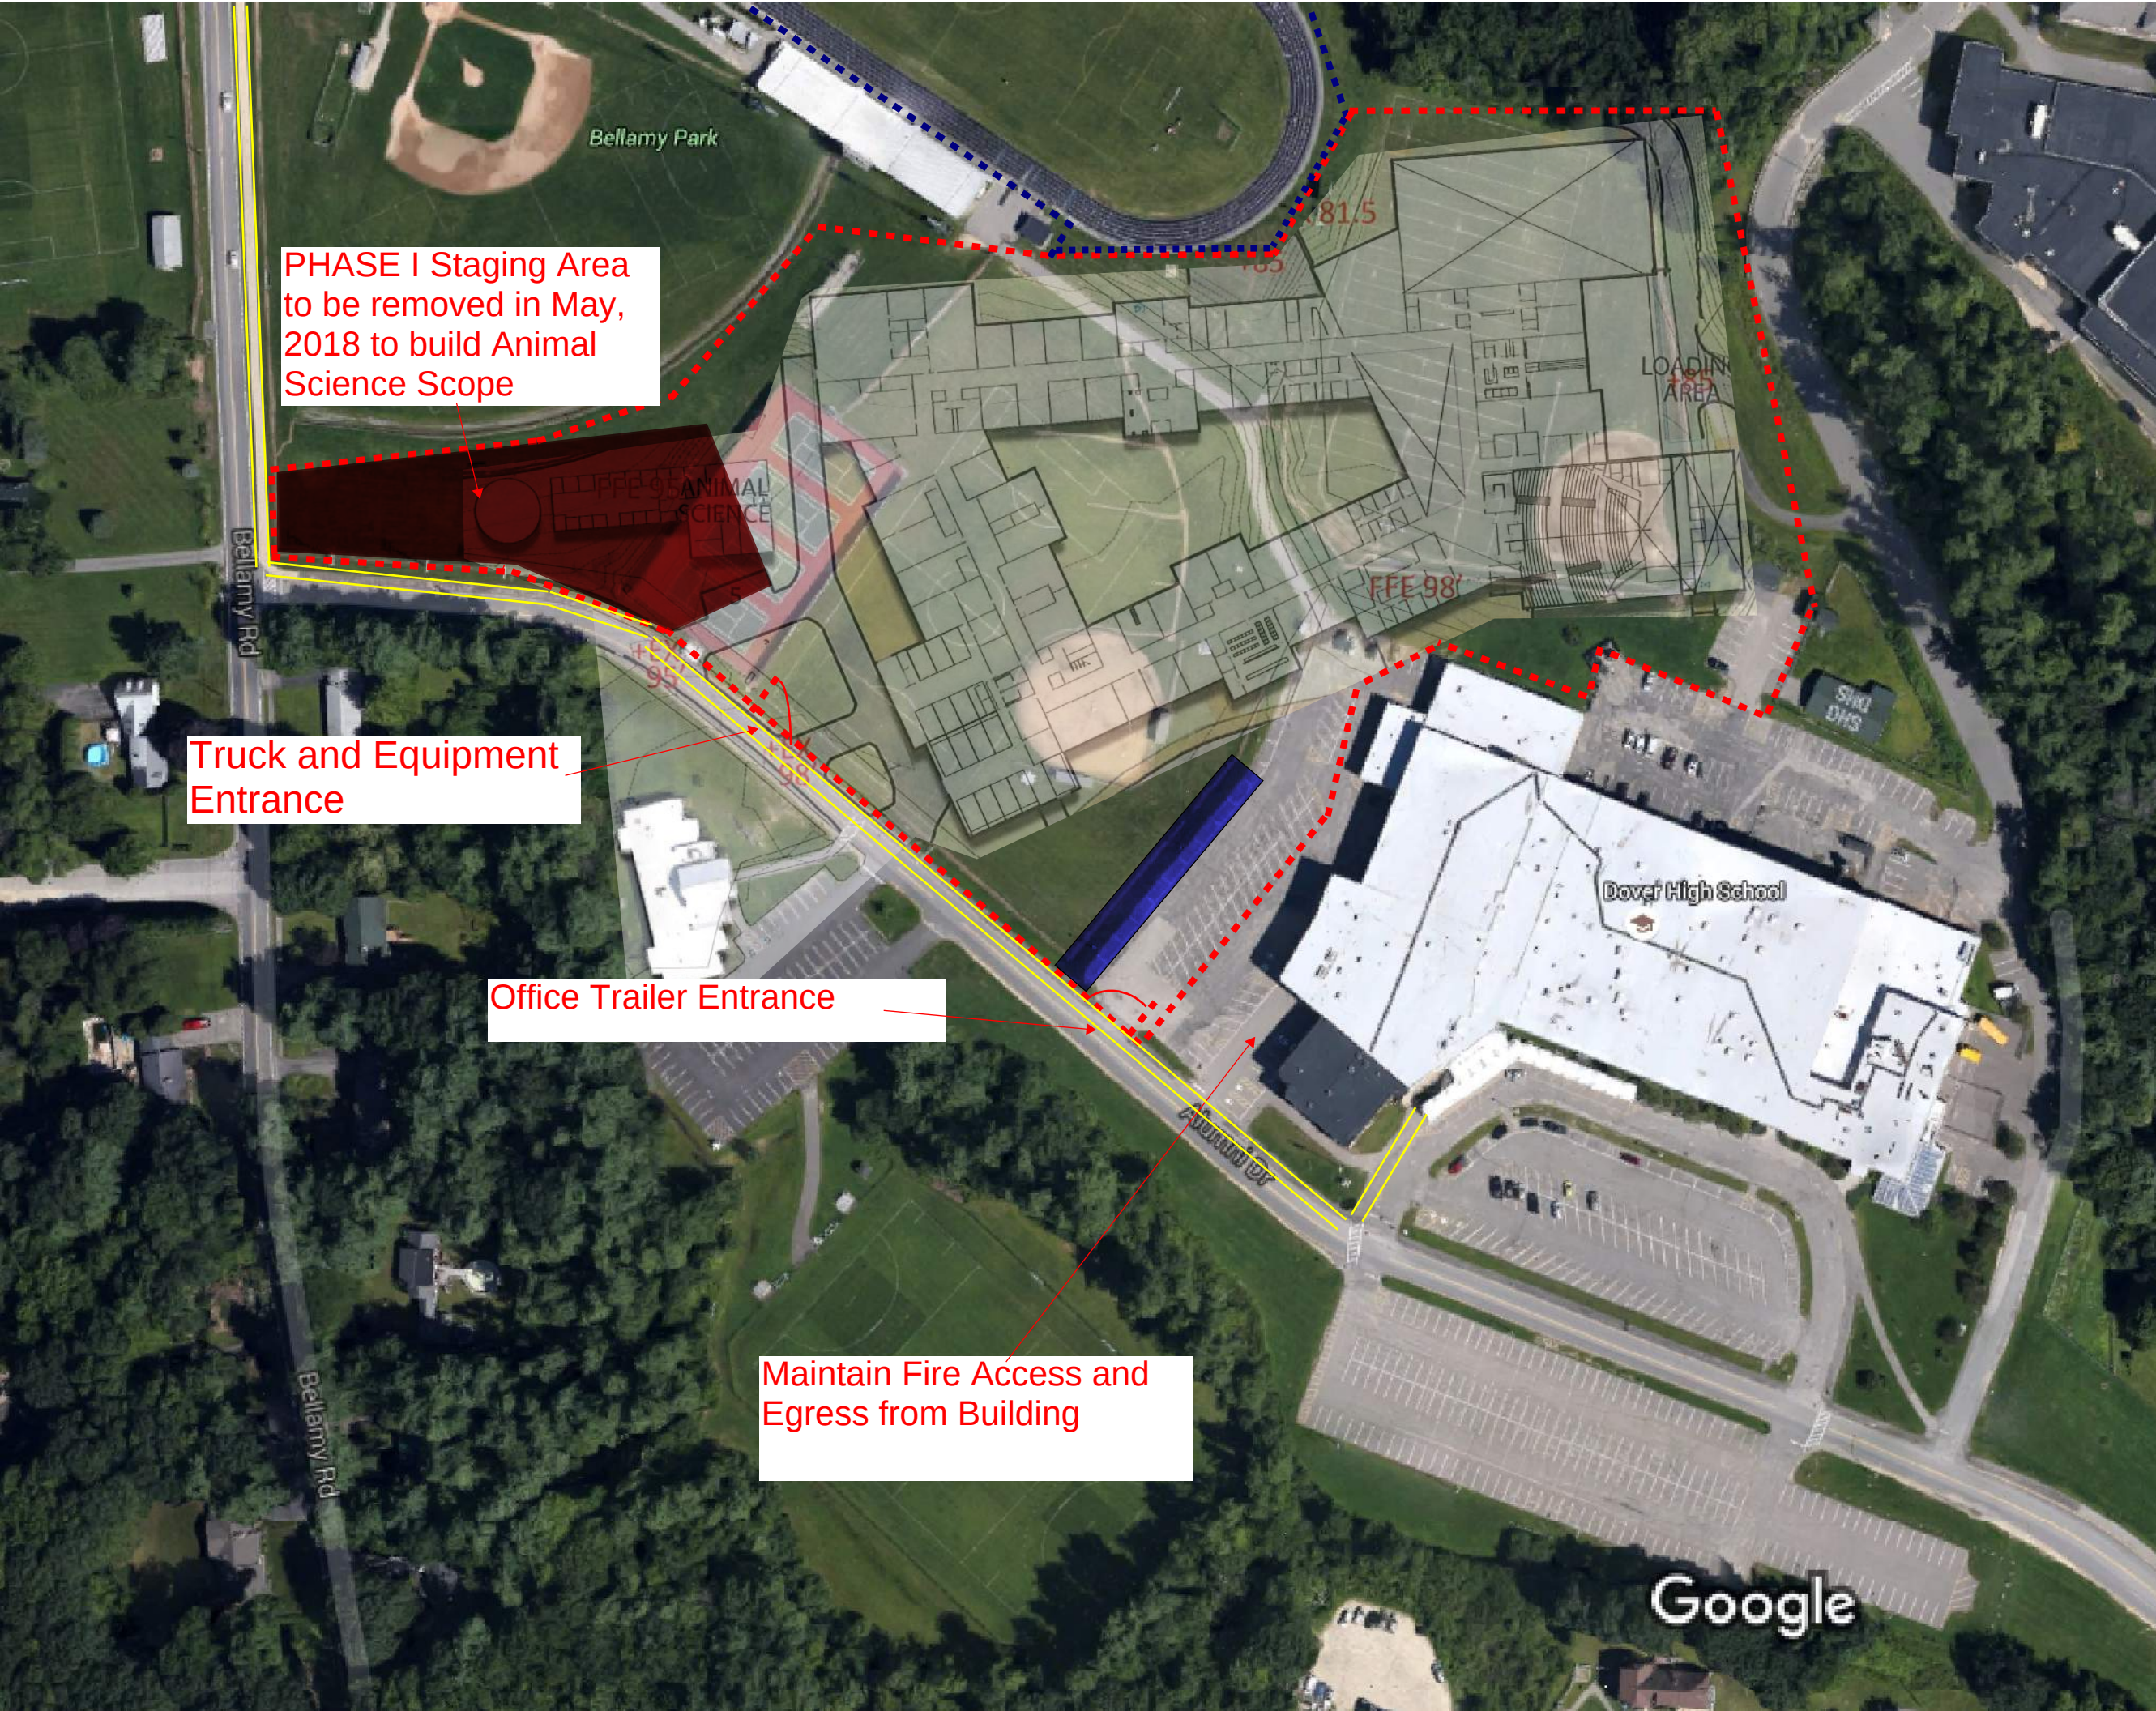

PHASE IA:
April thru Aug, 2106 Turf Field Install (Blue Fence Line)
Turf field scope will have a separate fence to be removed once field work is complete.

PHASE 1B:
June, 2016 thru Building Occupancy (Red Fence Line)
Site fence installed for preliminary site work and installation of subsurface improvements. Construction access points may be modified as necessary. Fencing adjacent to existing building shall be spaced to maintain proper egress from all building doors. Student Access to Fields shown as double yellow line. Extra signage placed at construction entrances.

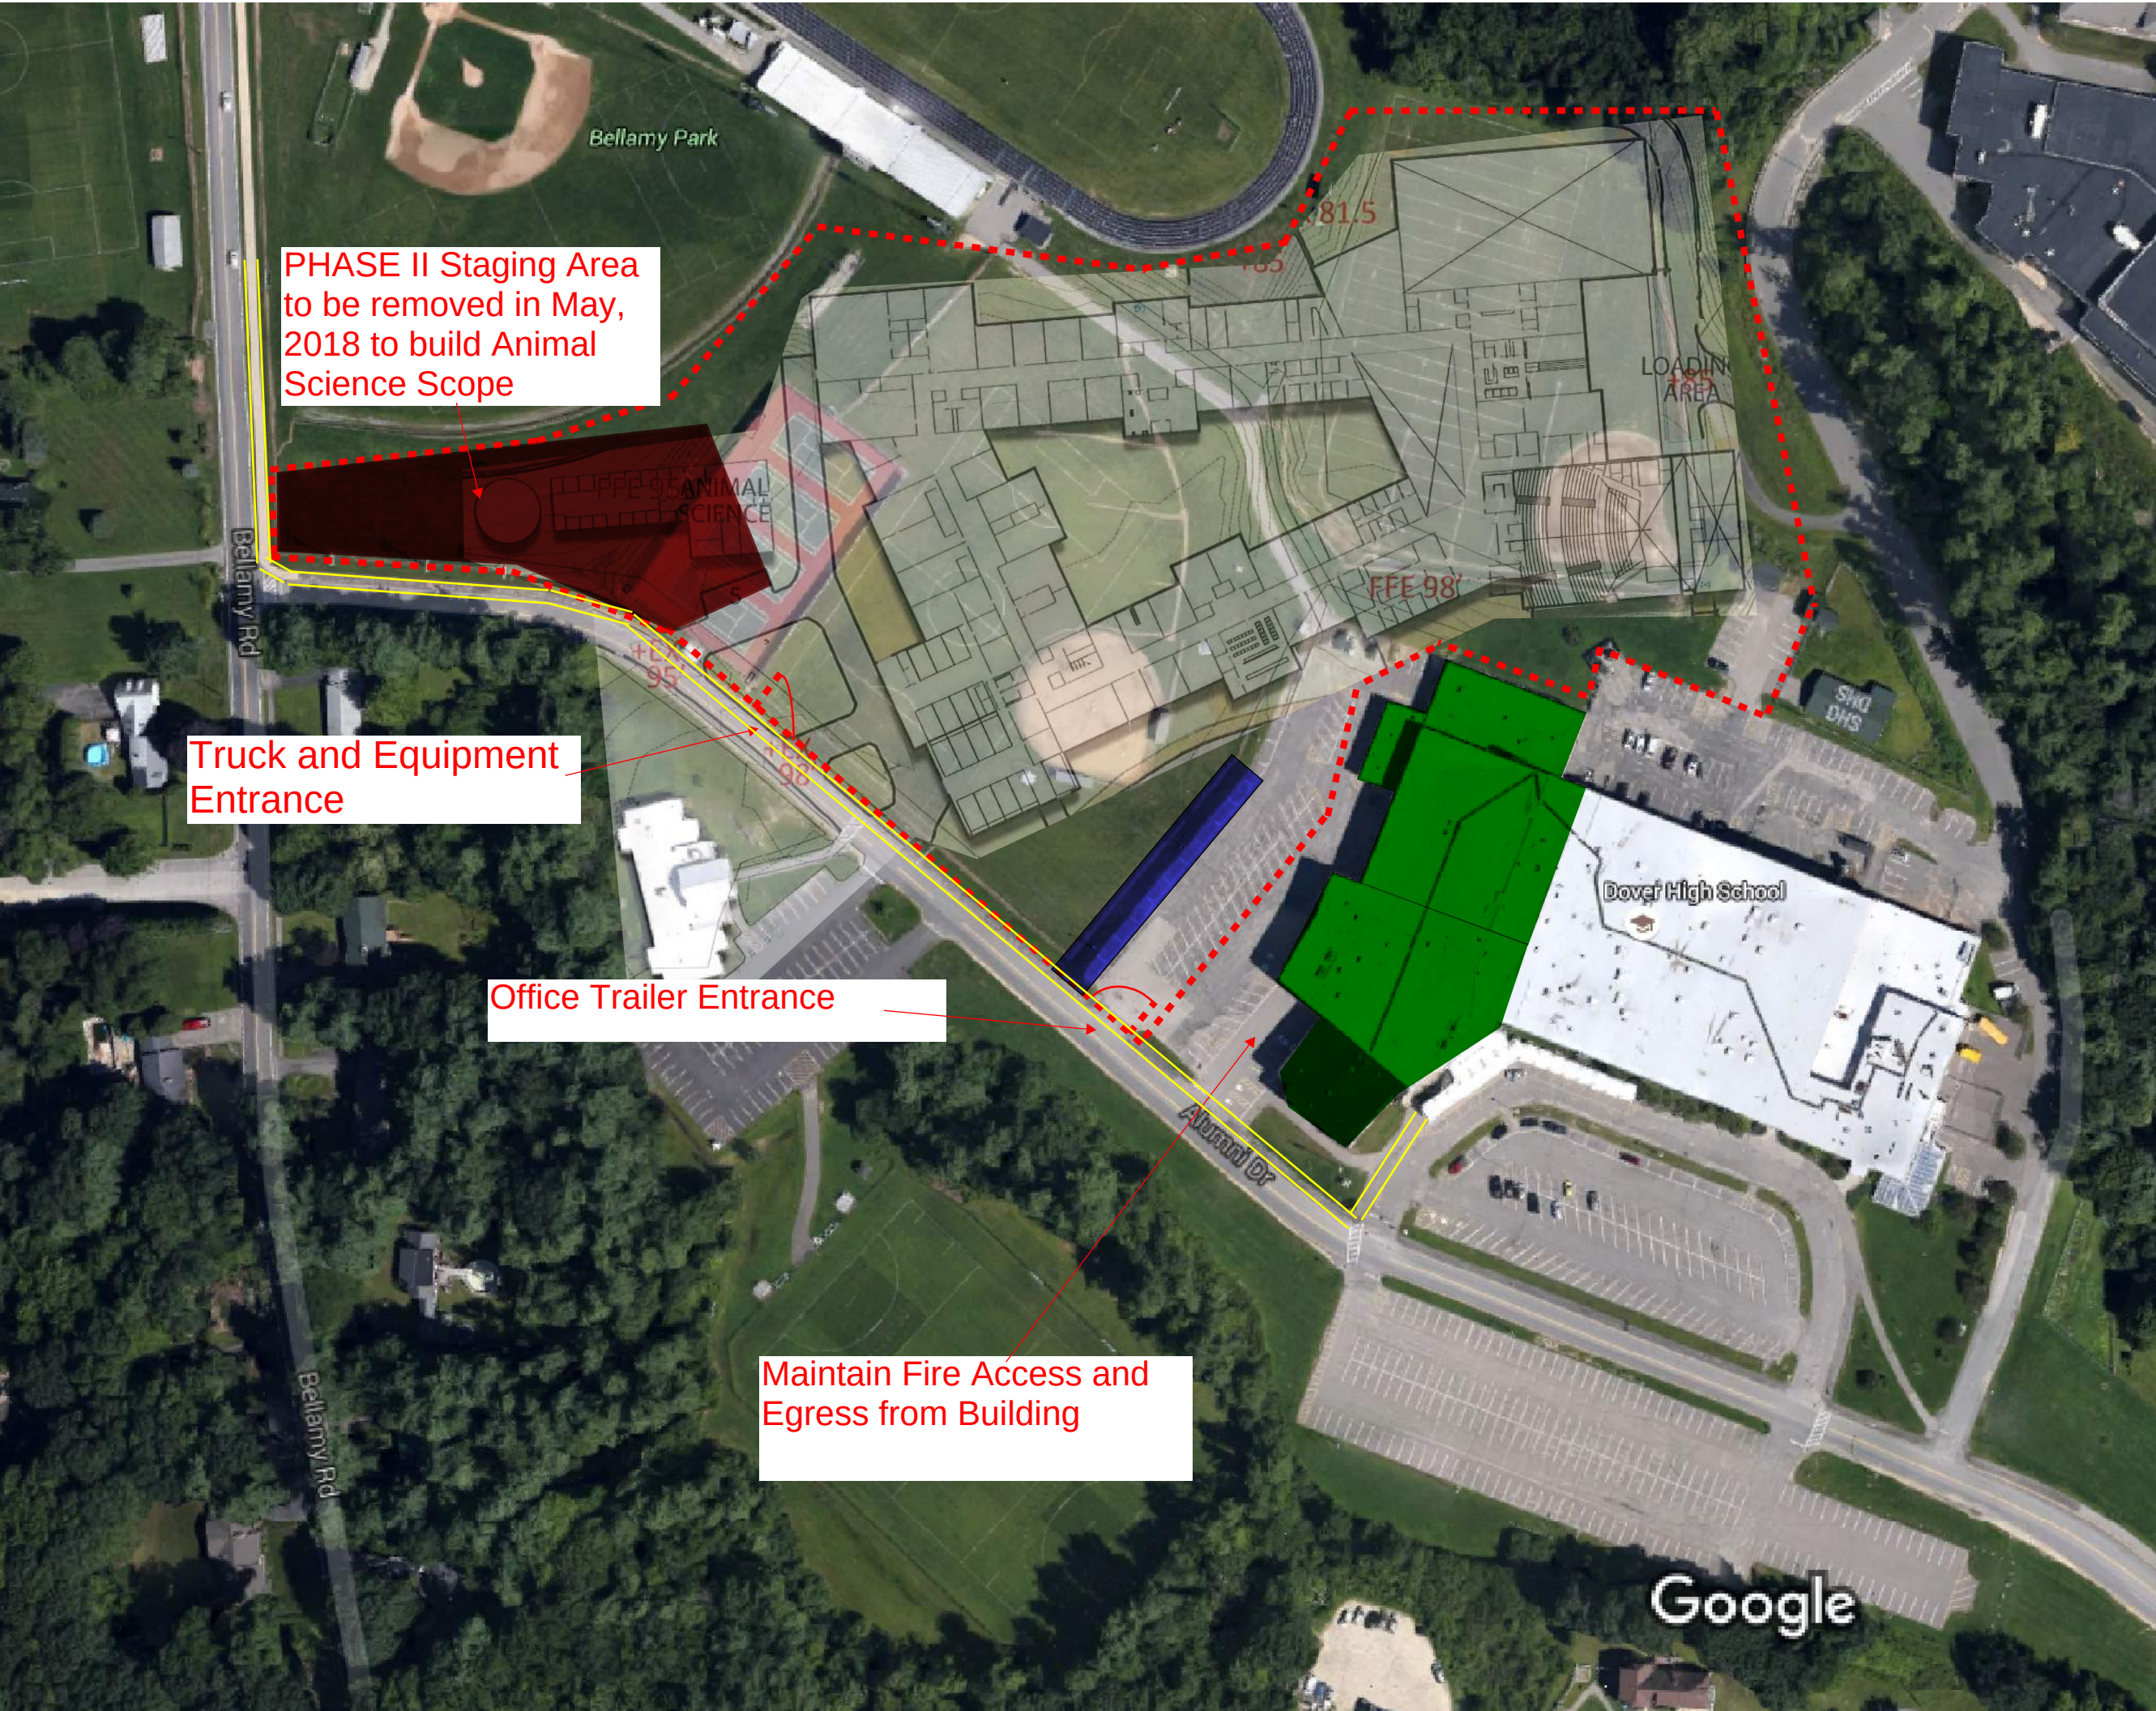


PHASE II:
Feb & April, 2018
Breaks
Perform Asbestos
Abatement and
restoration in Auditorium
during breaks.
Scope is dependent
upon final report from
Environmental
Consultant.

PHASE II Staging Area
to be removed in May,
2018 to build Animal
Science Scope

Truck and Equipment
Entrance

Office Trailer Entrance

Maintain Fire Access and
Egress from Building

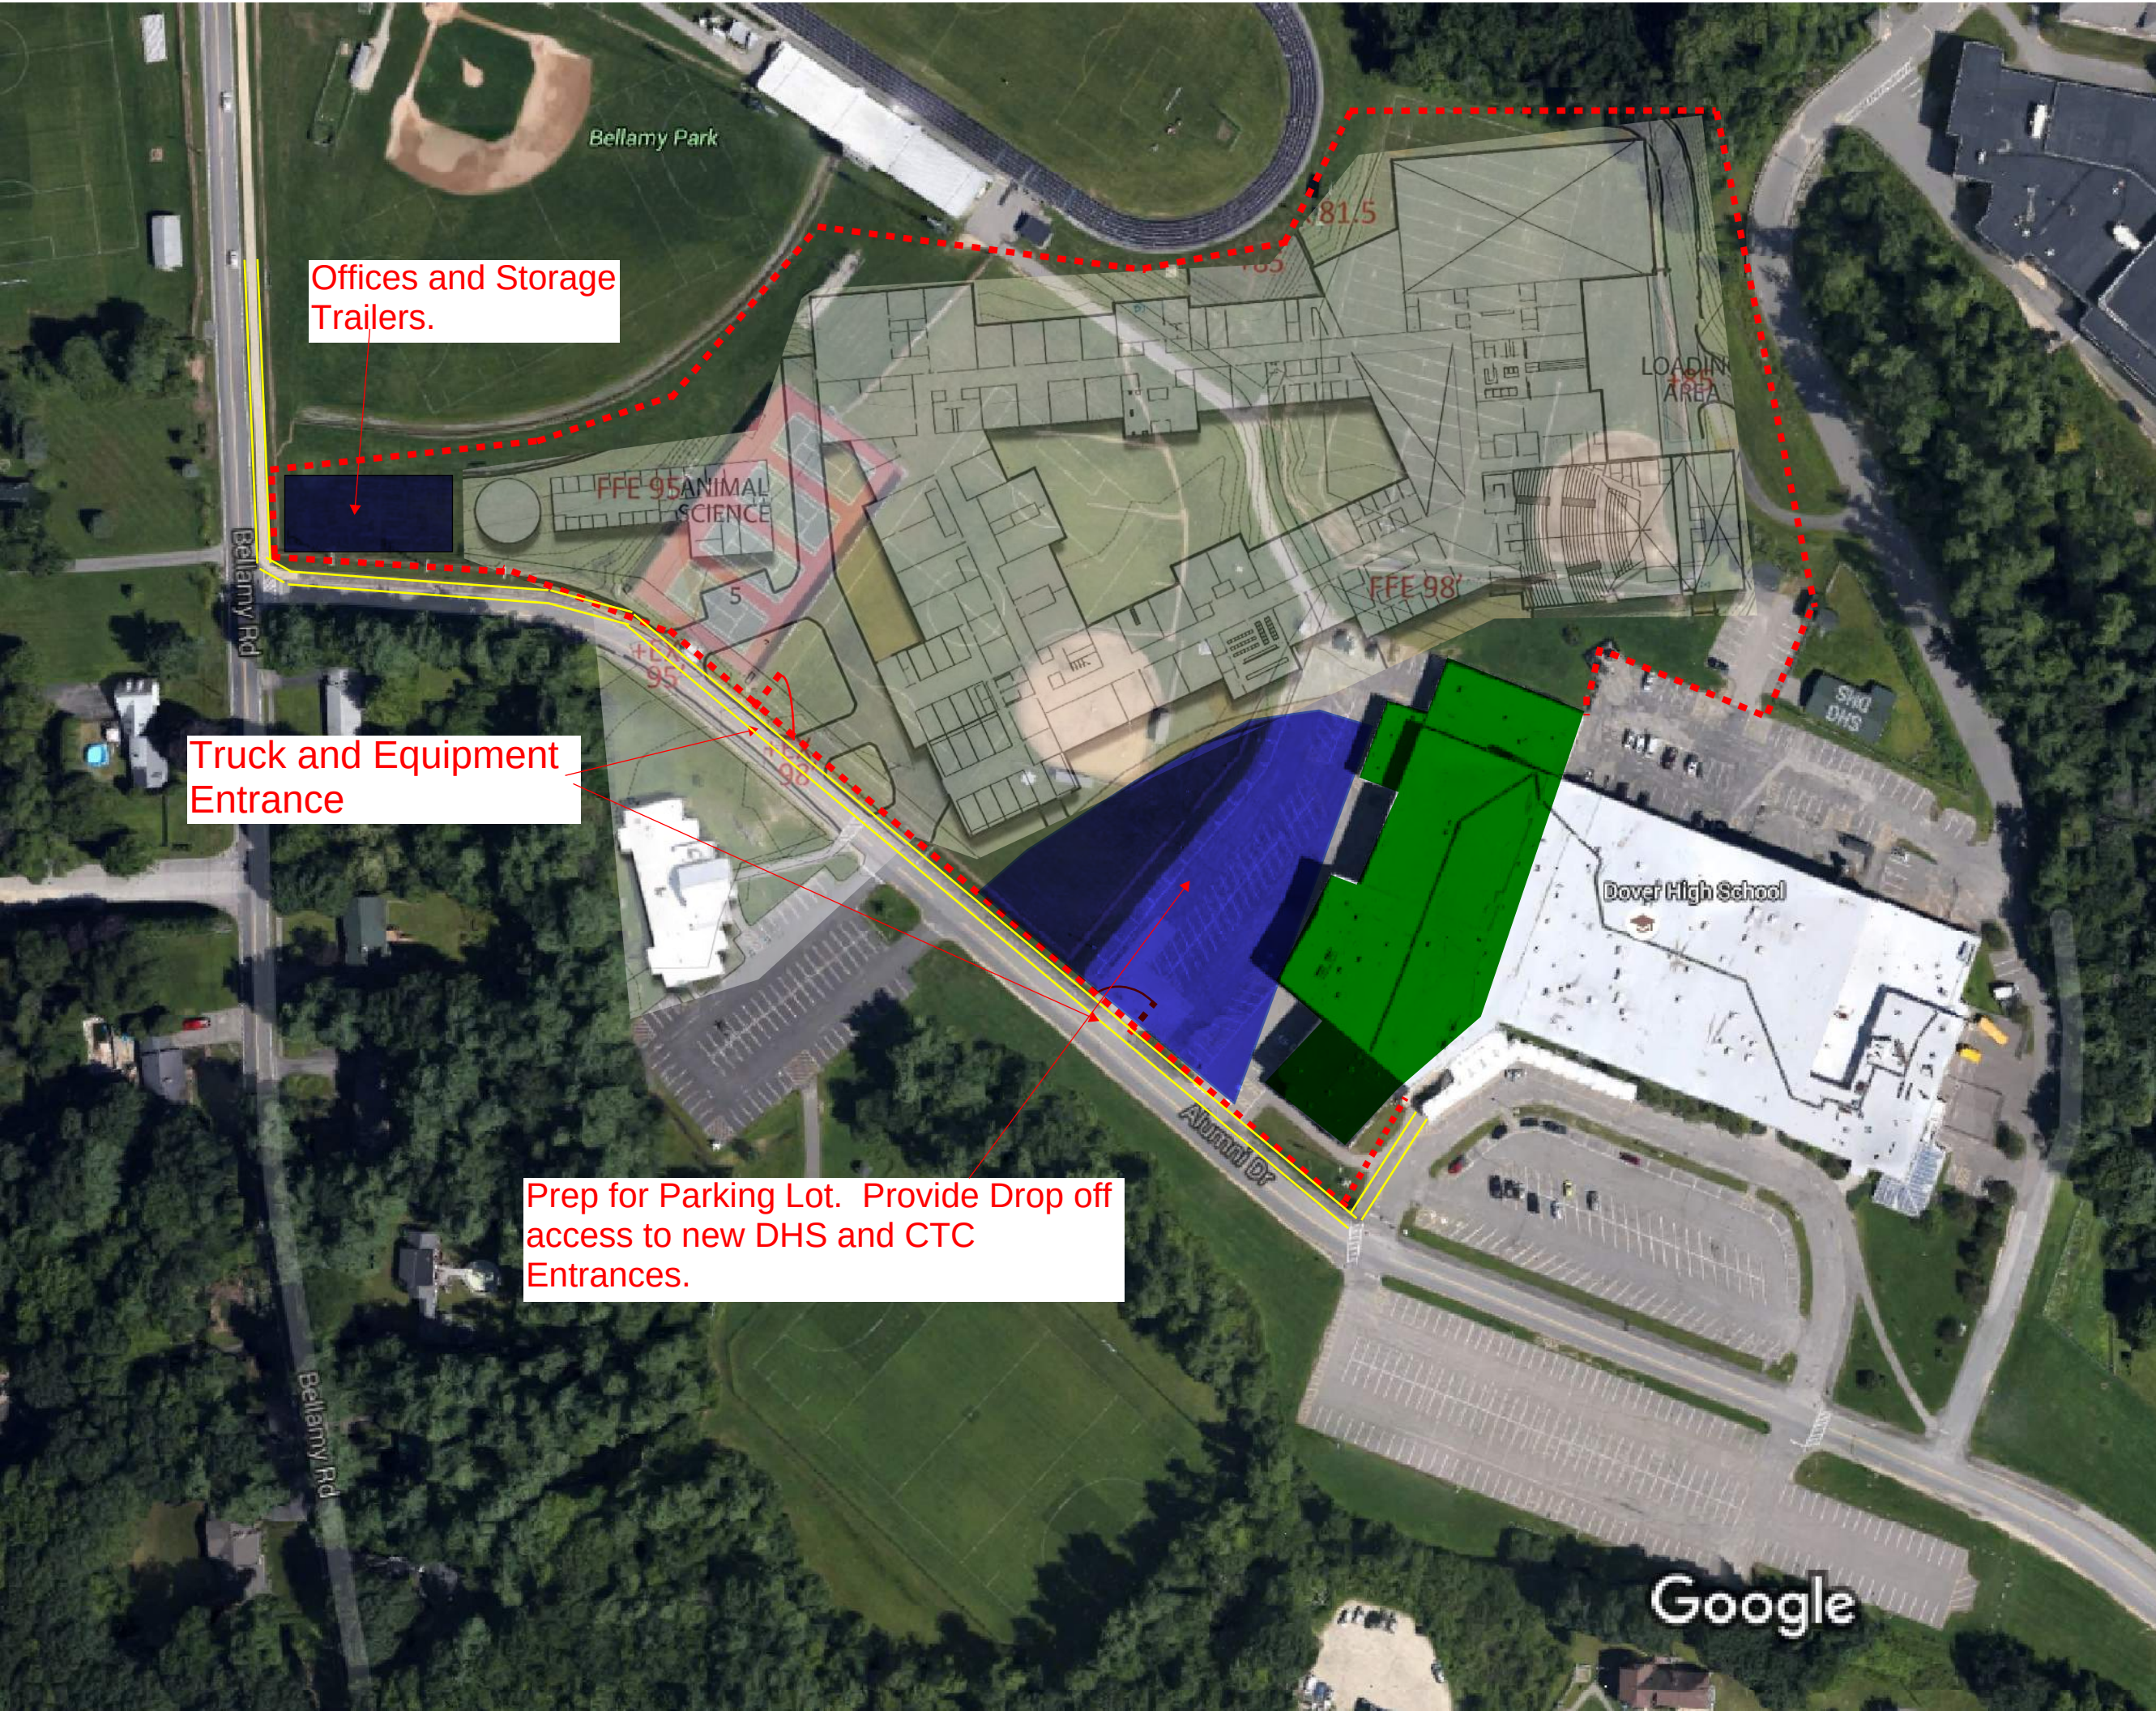


Offices and Storage Trailers.

Truck and Equipment Entrance

Prep for Parking Lot. Provide Drop off access to new DHS and CTC Entrances.

PHASE III:
June thru Aug, 2018
Demolition of existing Auditorium and Gymnasium.
Prep for Westerly Parking Lot.

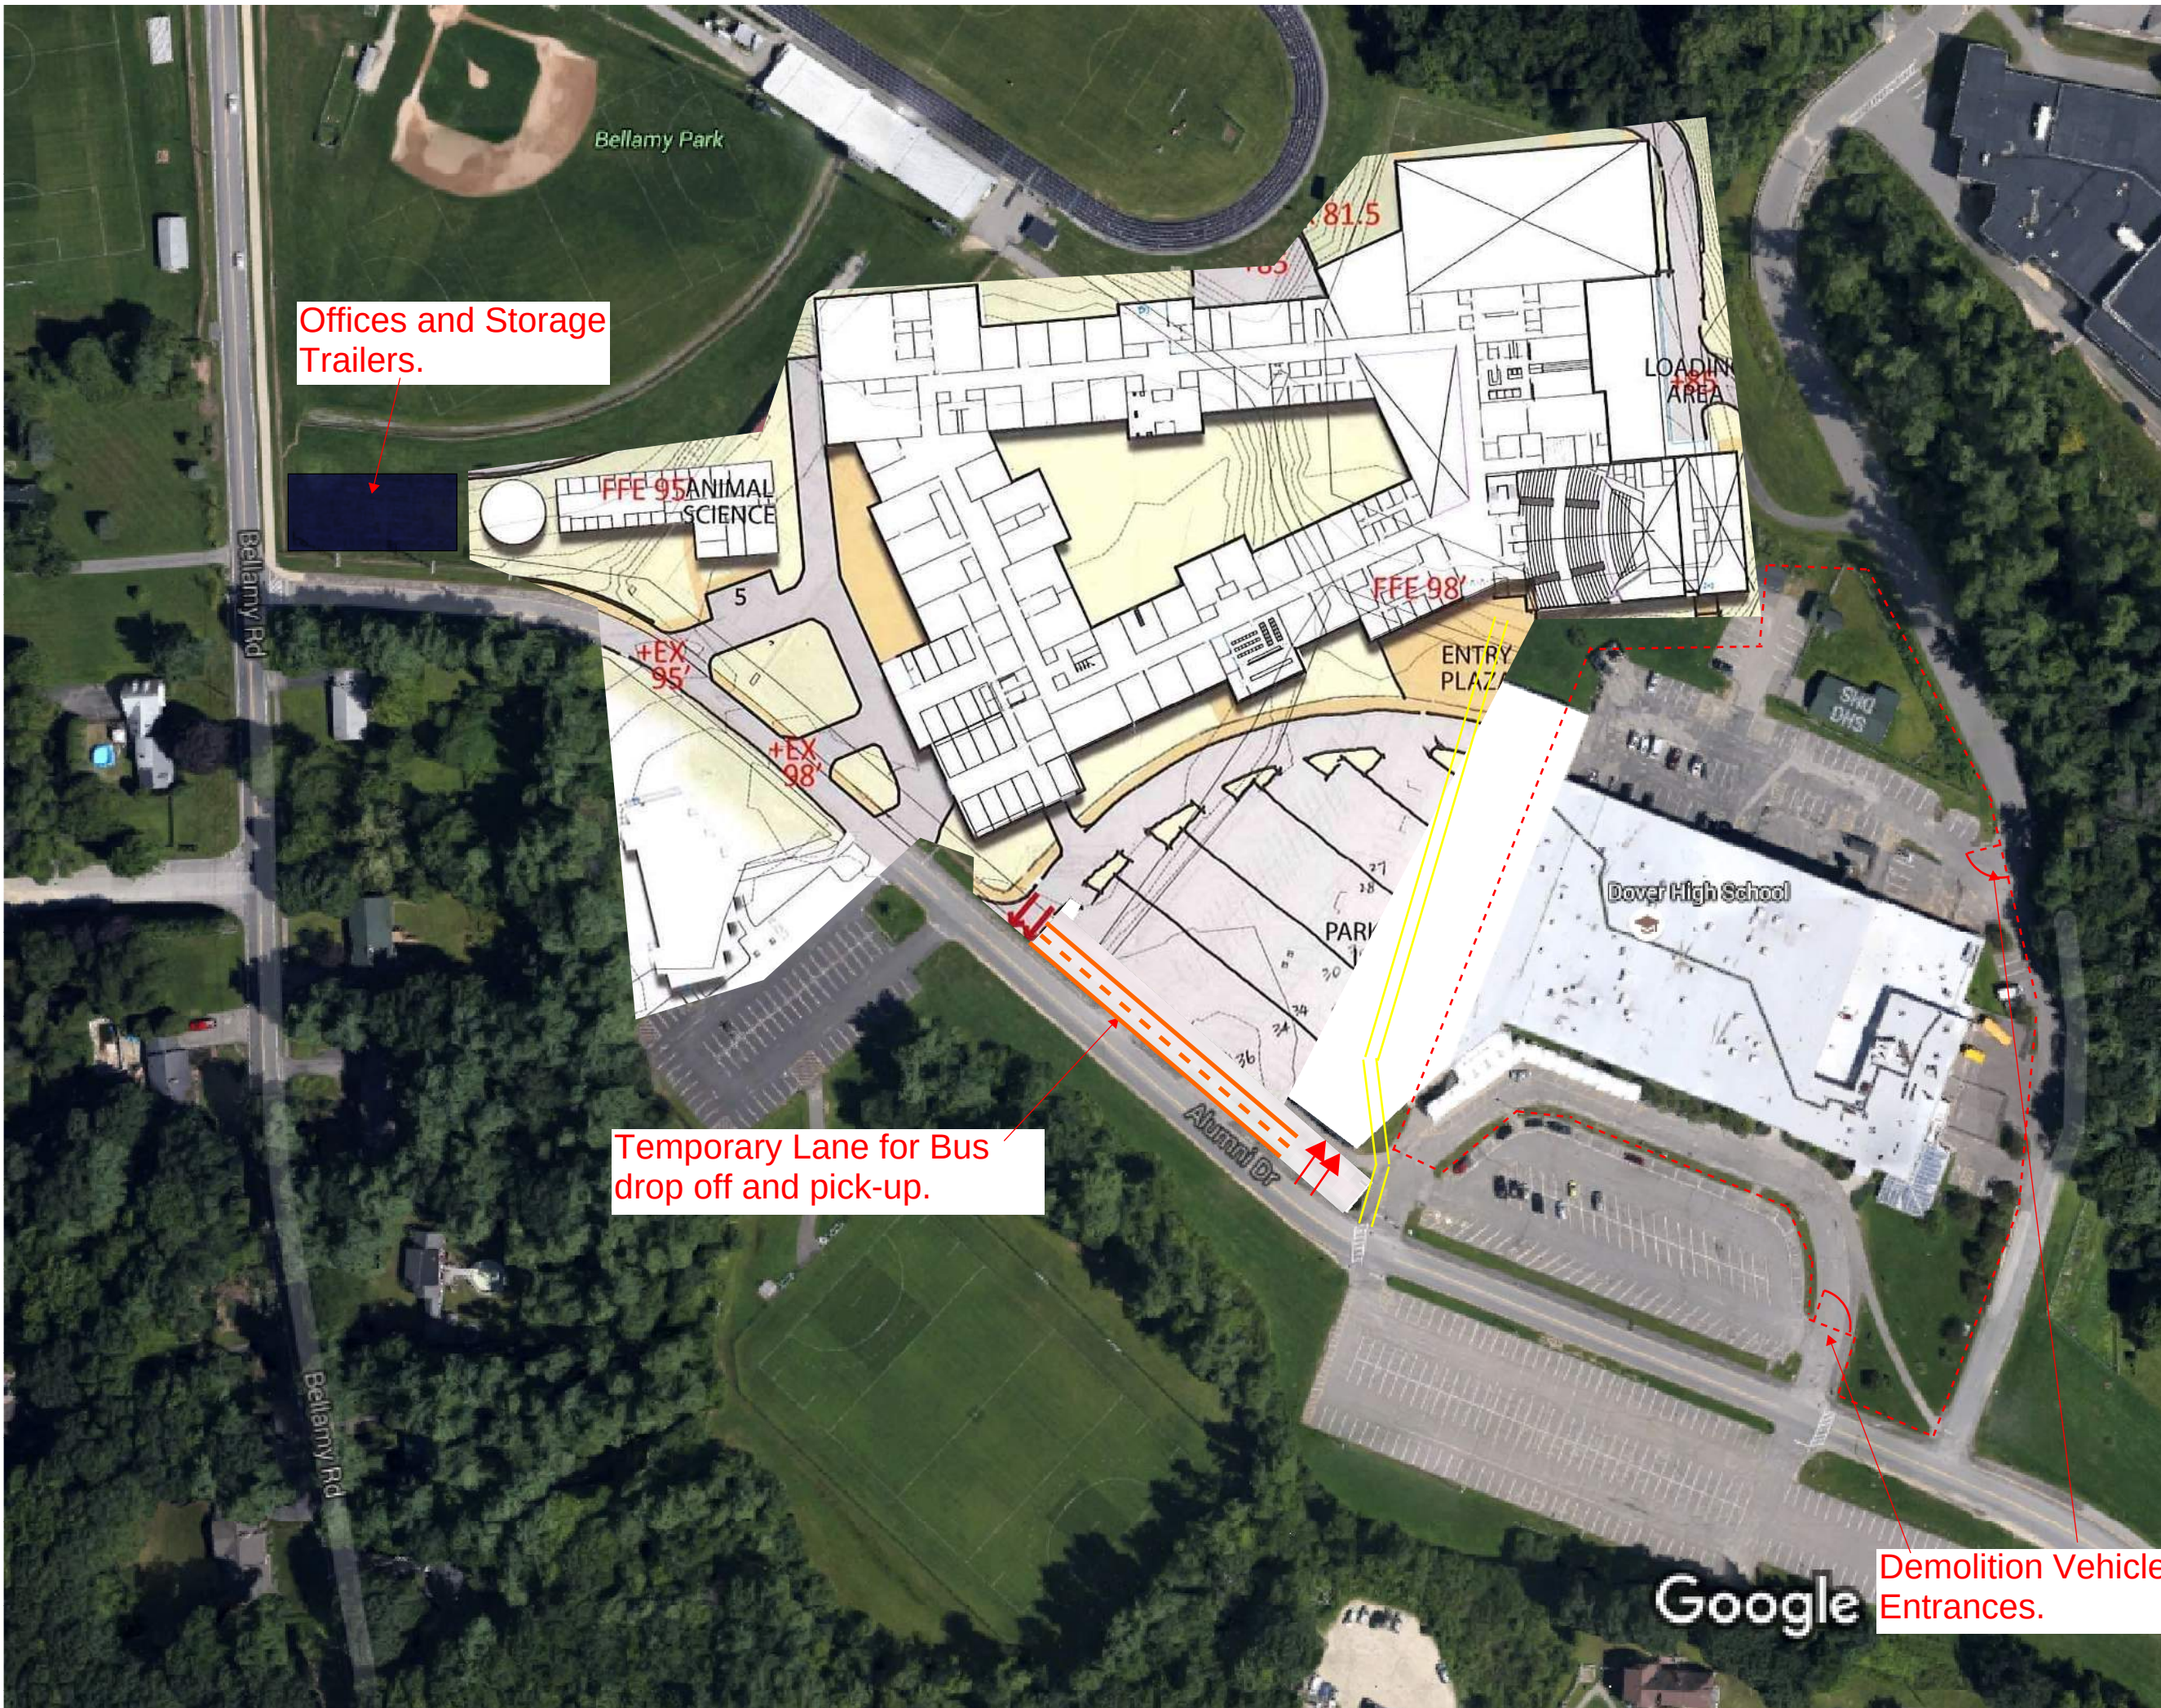


Offices and Storage Trailers.



Temporary Lane for Bus drop off and pick-up.

Demolition Vehicle Entrances.

PHASE IV:
Sept, 2018 thru March, 2019
Demolition of Existing High School and CTC Structure. Existing South Lots remain in service during demolition. Westerly portion of new lot limited to staff parking and pedestrian access to new building. Final configuration of completed lot to be modified as construction progresses.

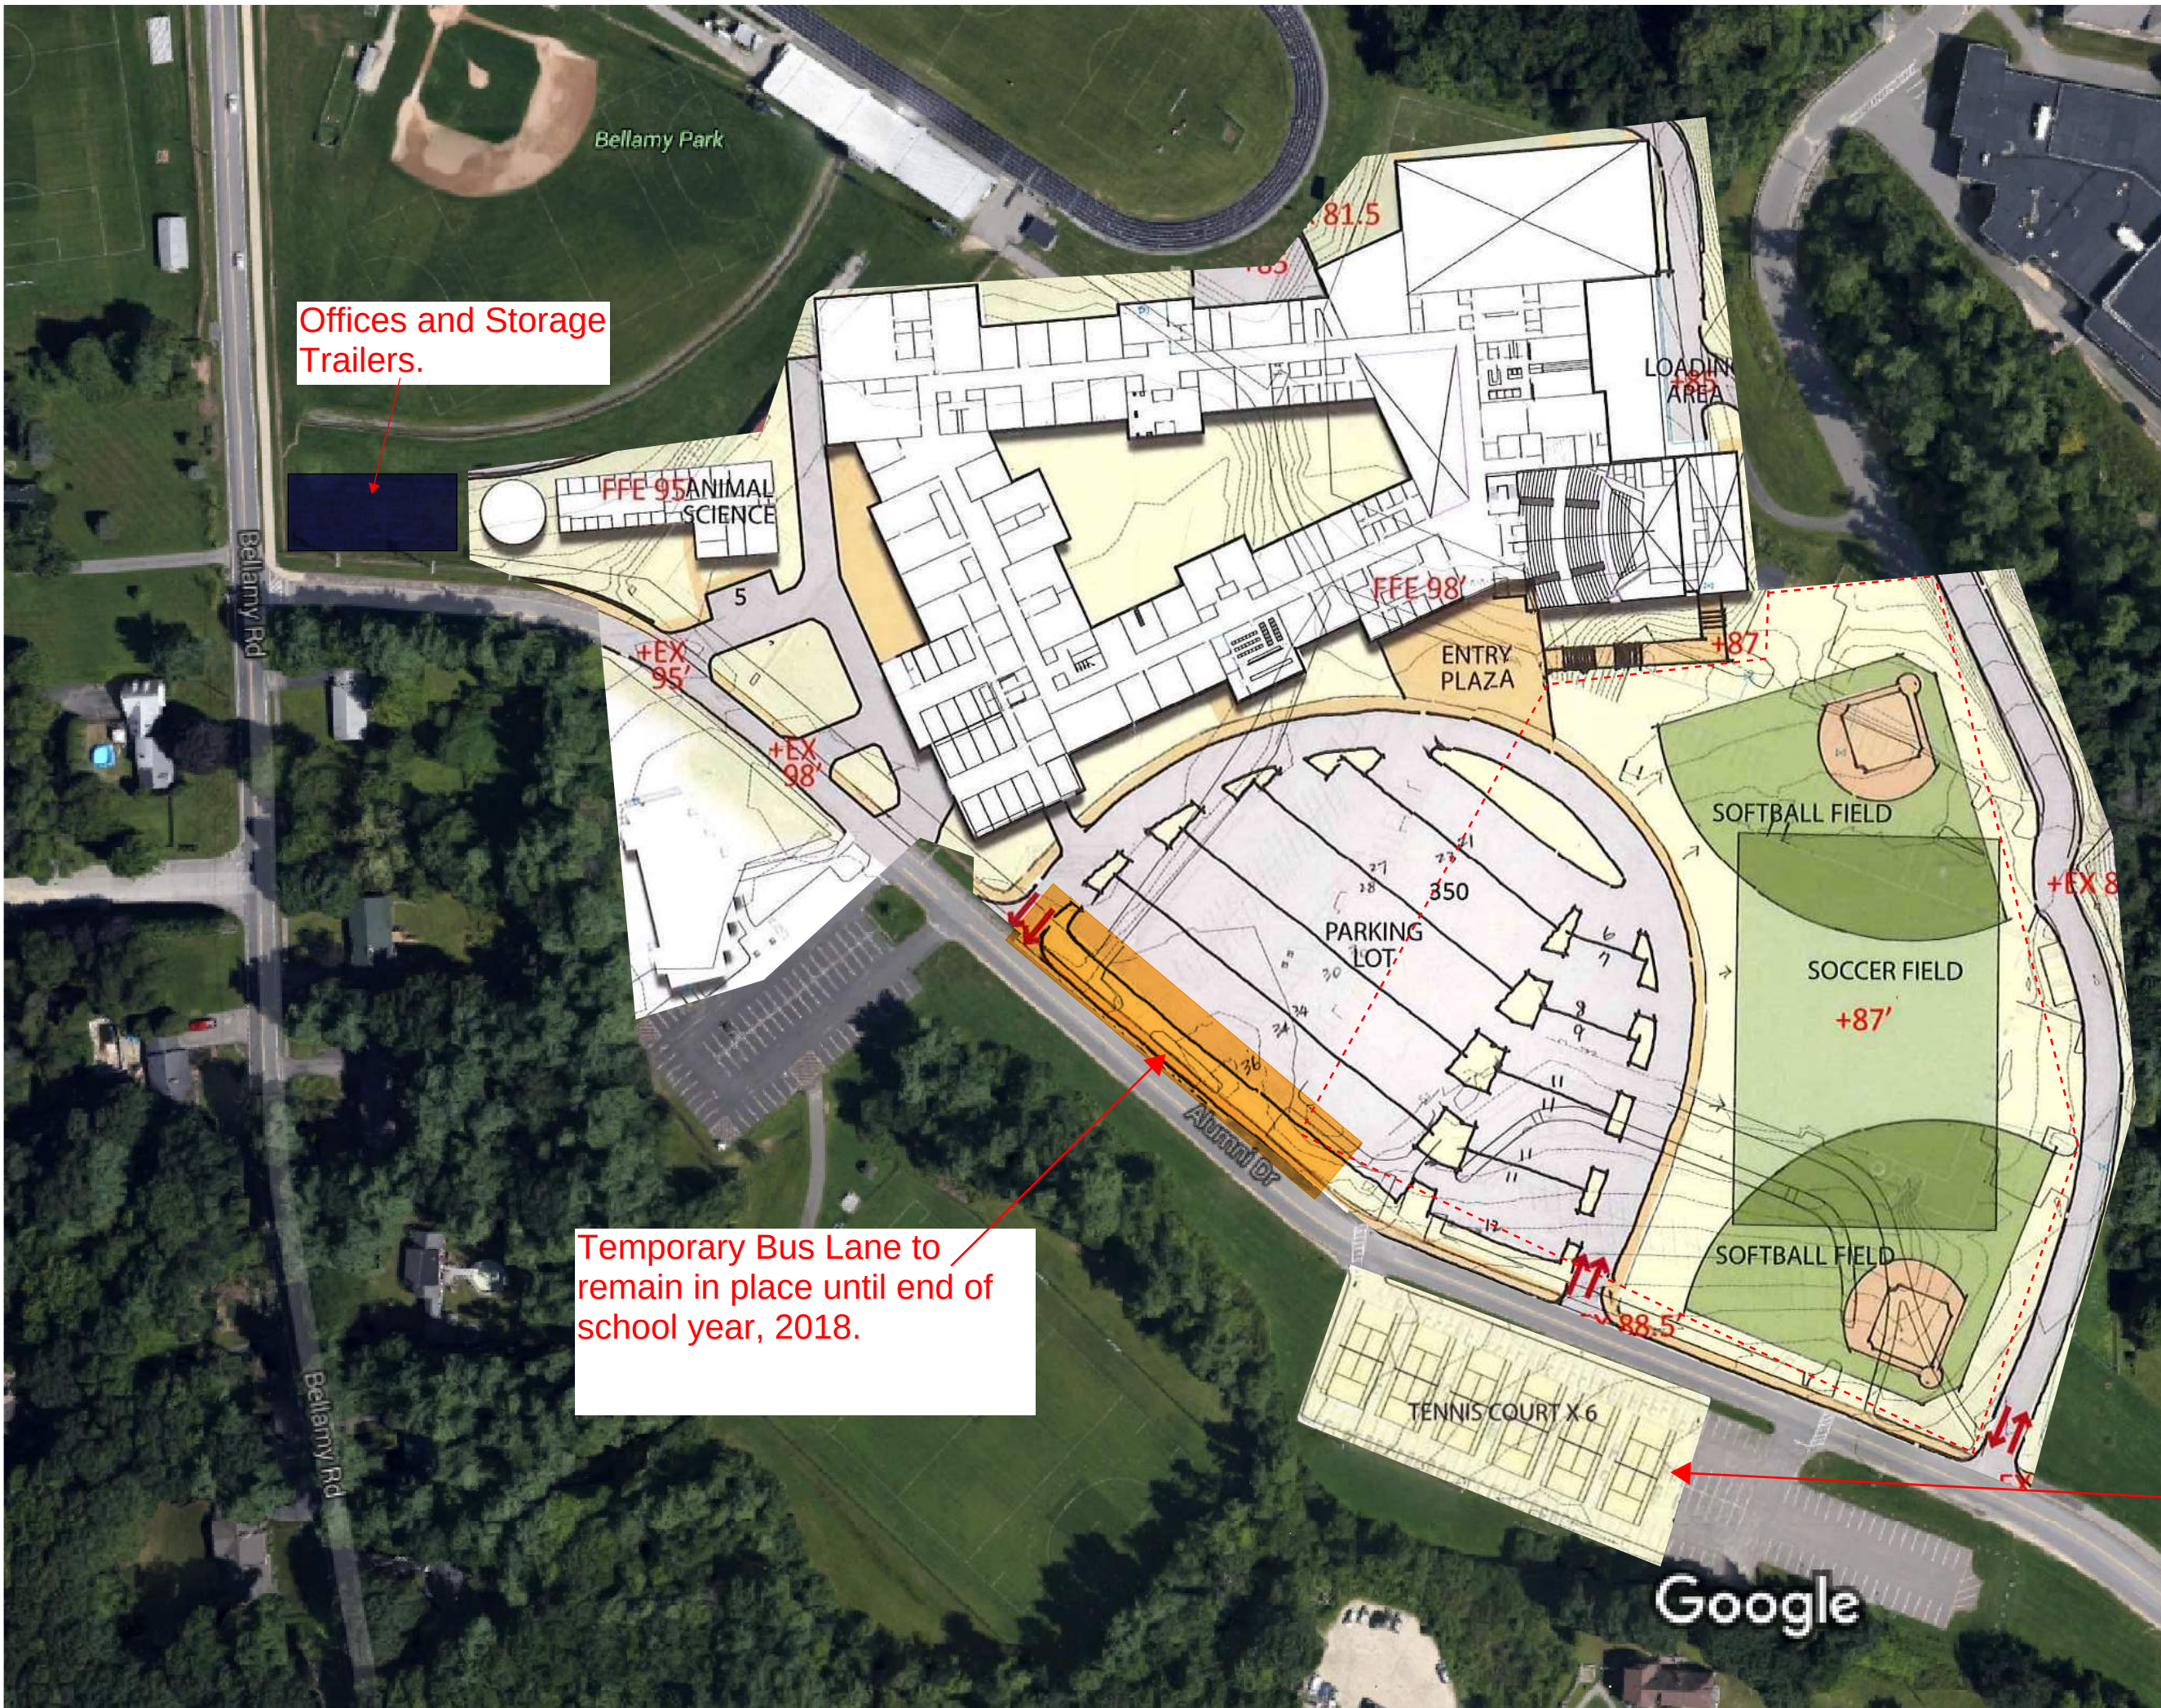

Offices and Storage Trailers.

Temporary Bus Lane to remain in place until end of school year, 2018.

PHASE V:
Apr, 2019 thru Aug, 2019
Construction of remaining section of new parking lot.
Construction of new softball and soccer fields.
Reconfiguration of roadways as necessary. Parking lot south of Alumni Drive would remain in service for duration of work.
Fields would not be available for Fall, 2019 sports.

PHASE VI:
New tennis court work to begin once new parking lot is complete on north side of Alumni Drive.
