


PHASE I:
Turf Field
April, 2016 thru June, 2016
Track and Football Field operational by
8/11/16.
Fence and access plan will be modified
once Phase II begins.



Temp fence around inside
of track. Fence location to
be coordinated with final
turf field layout.

Access road for turf field
work.

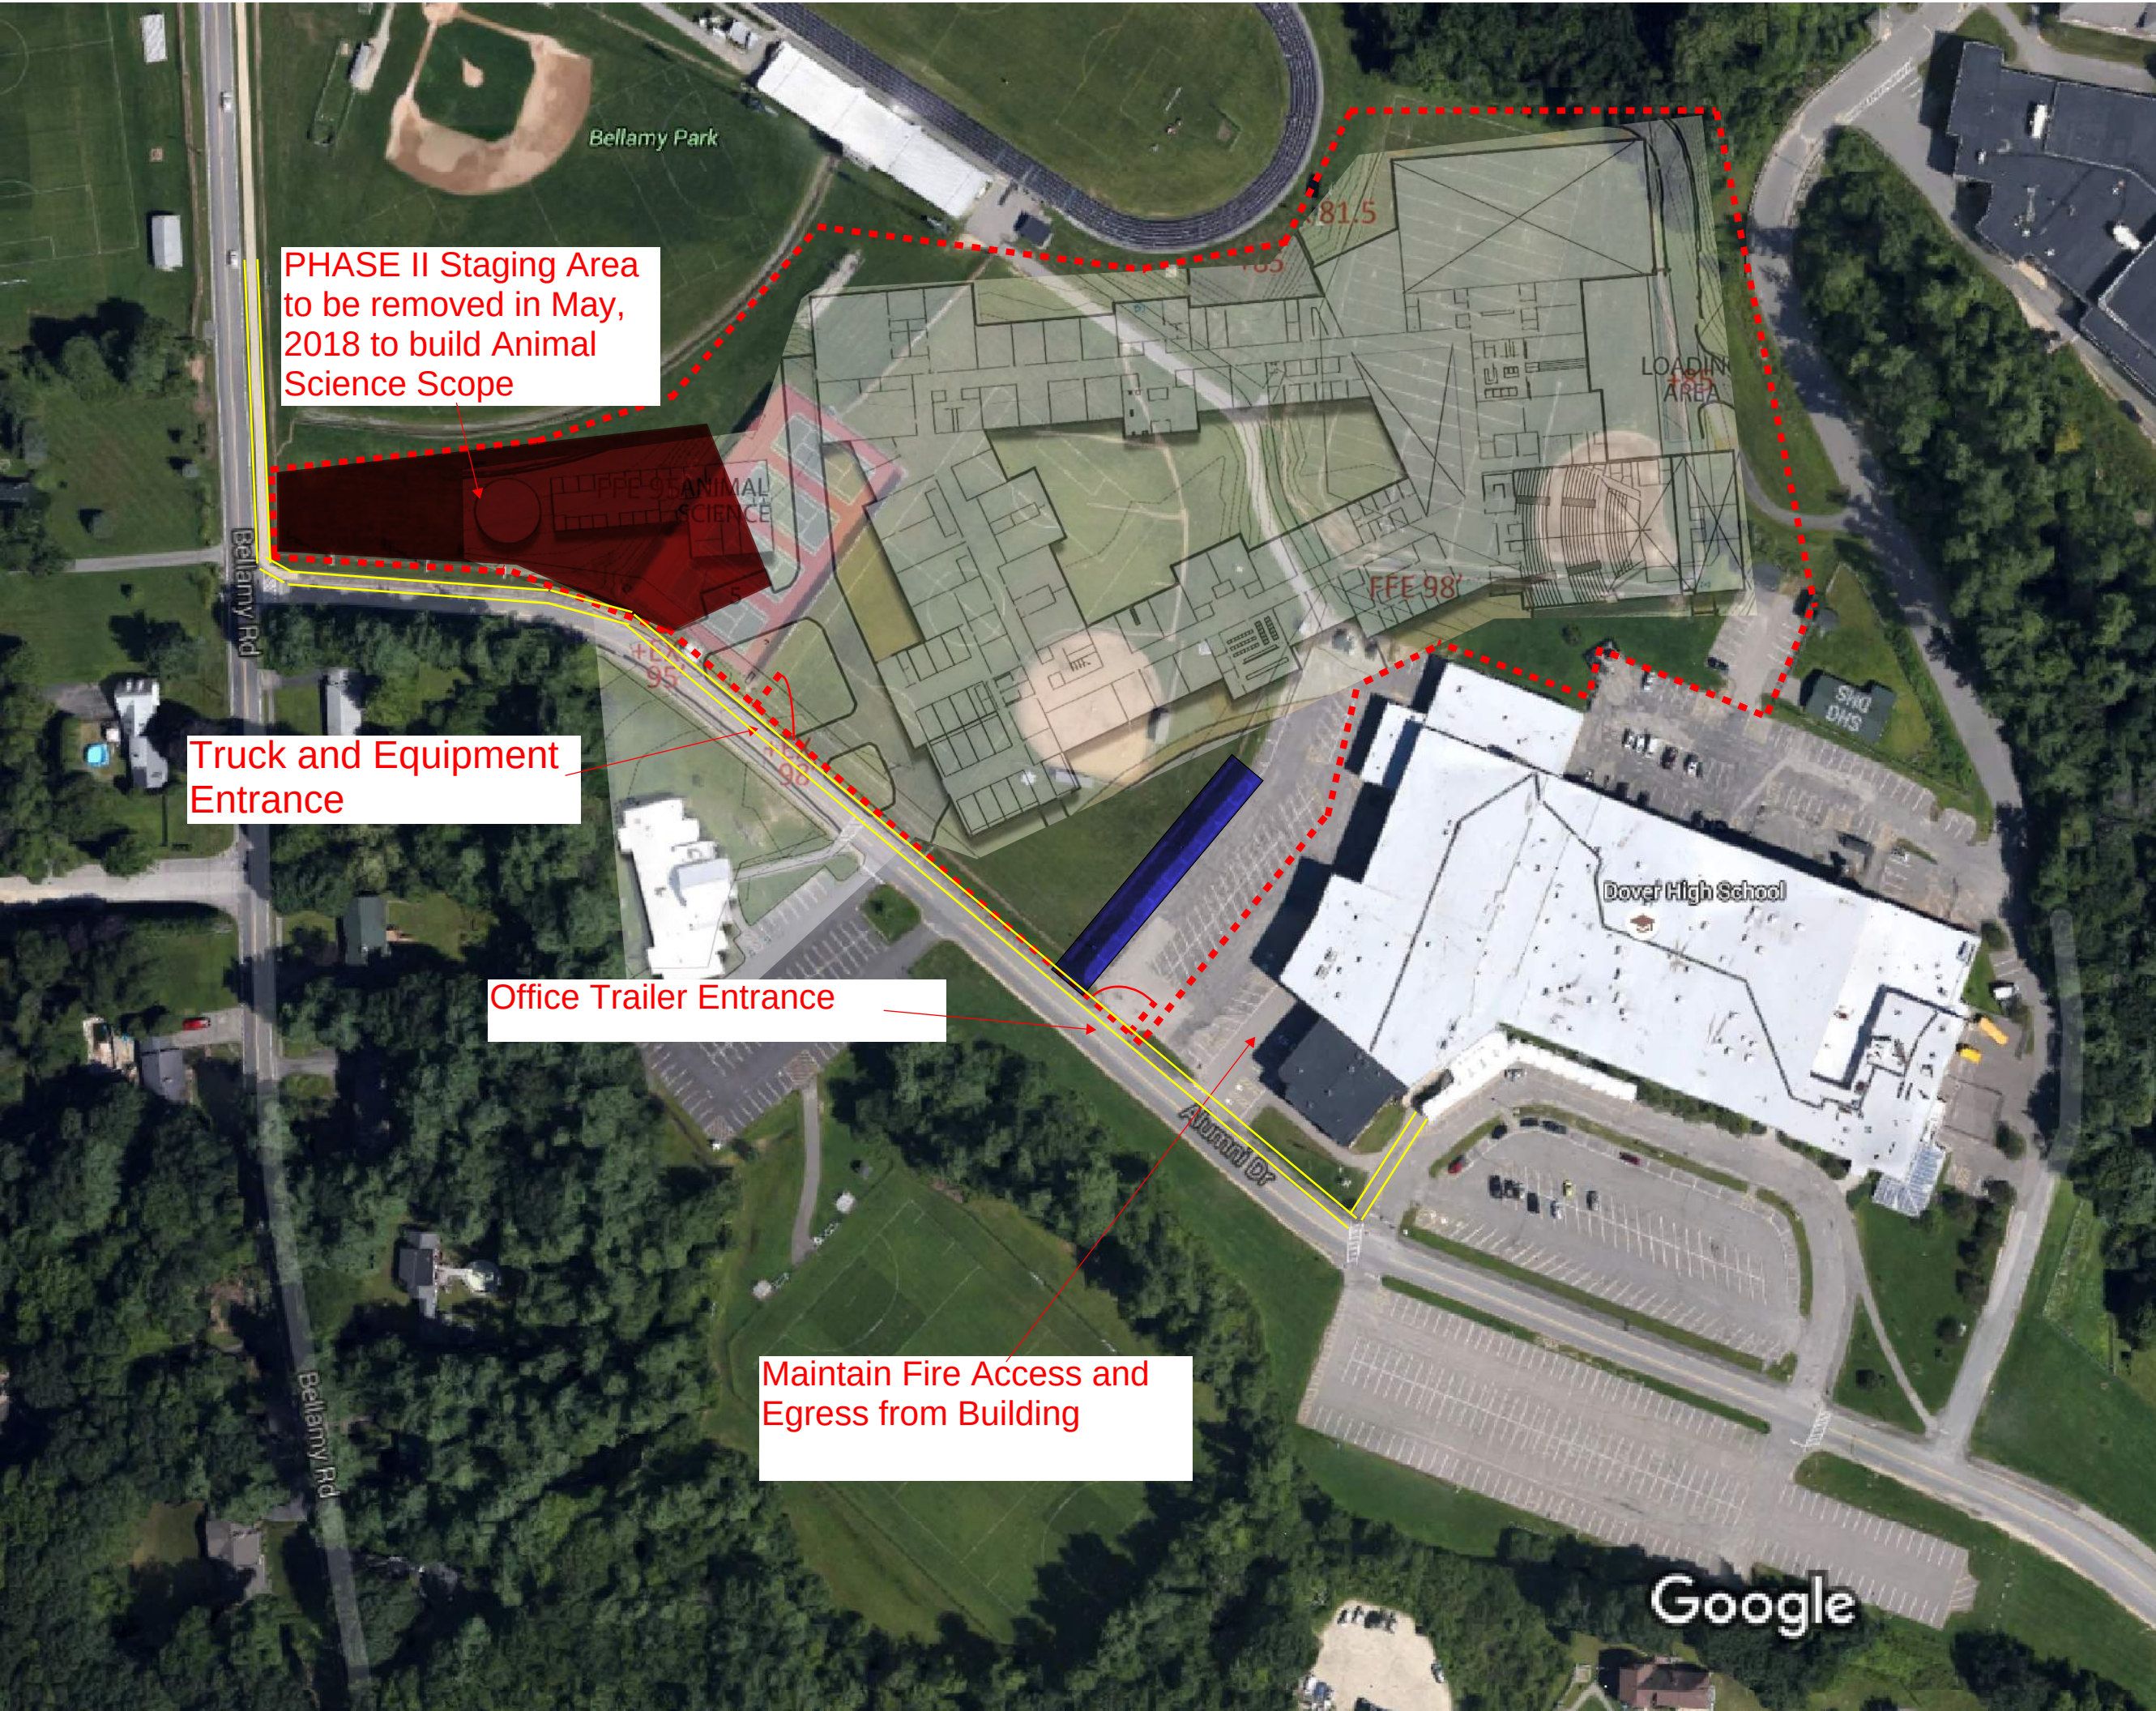


PHASE II Staging Area
to be removed in May,
2018 to build Animal
Science Scope

Truck and Equipment
Entrance

Office Trailer Entrance

Maintain Fire Access and
Egress from Building

PHASE II:
June, 2016 thru Building
Occupancy (Red Fence
Line)
Site fence installed for
preliminary site work
and installation of
subsurface
improvements.
Construction access
points may be modified
as necessary.
Fencing adjacent to
existing building shall be
spaced to maintain
proper egress from all
building doors.
Student Access to
Fields shown as double
yellow line. Extra
signage placed at
construction entrances.

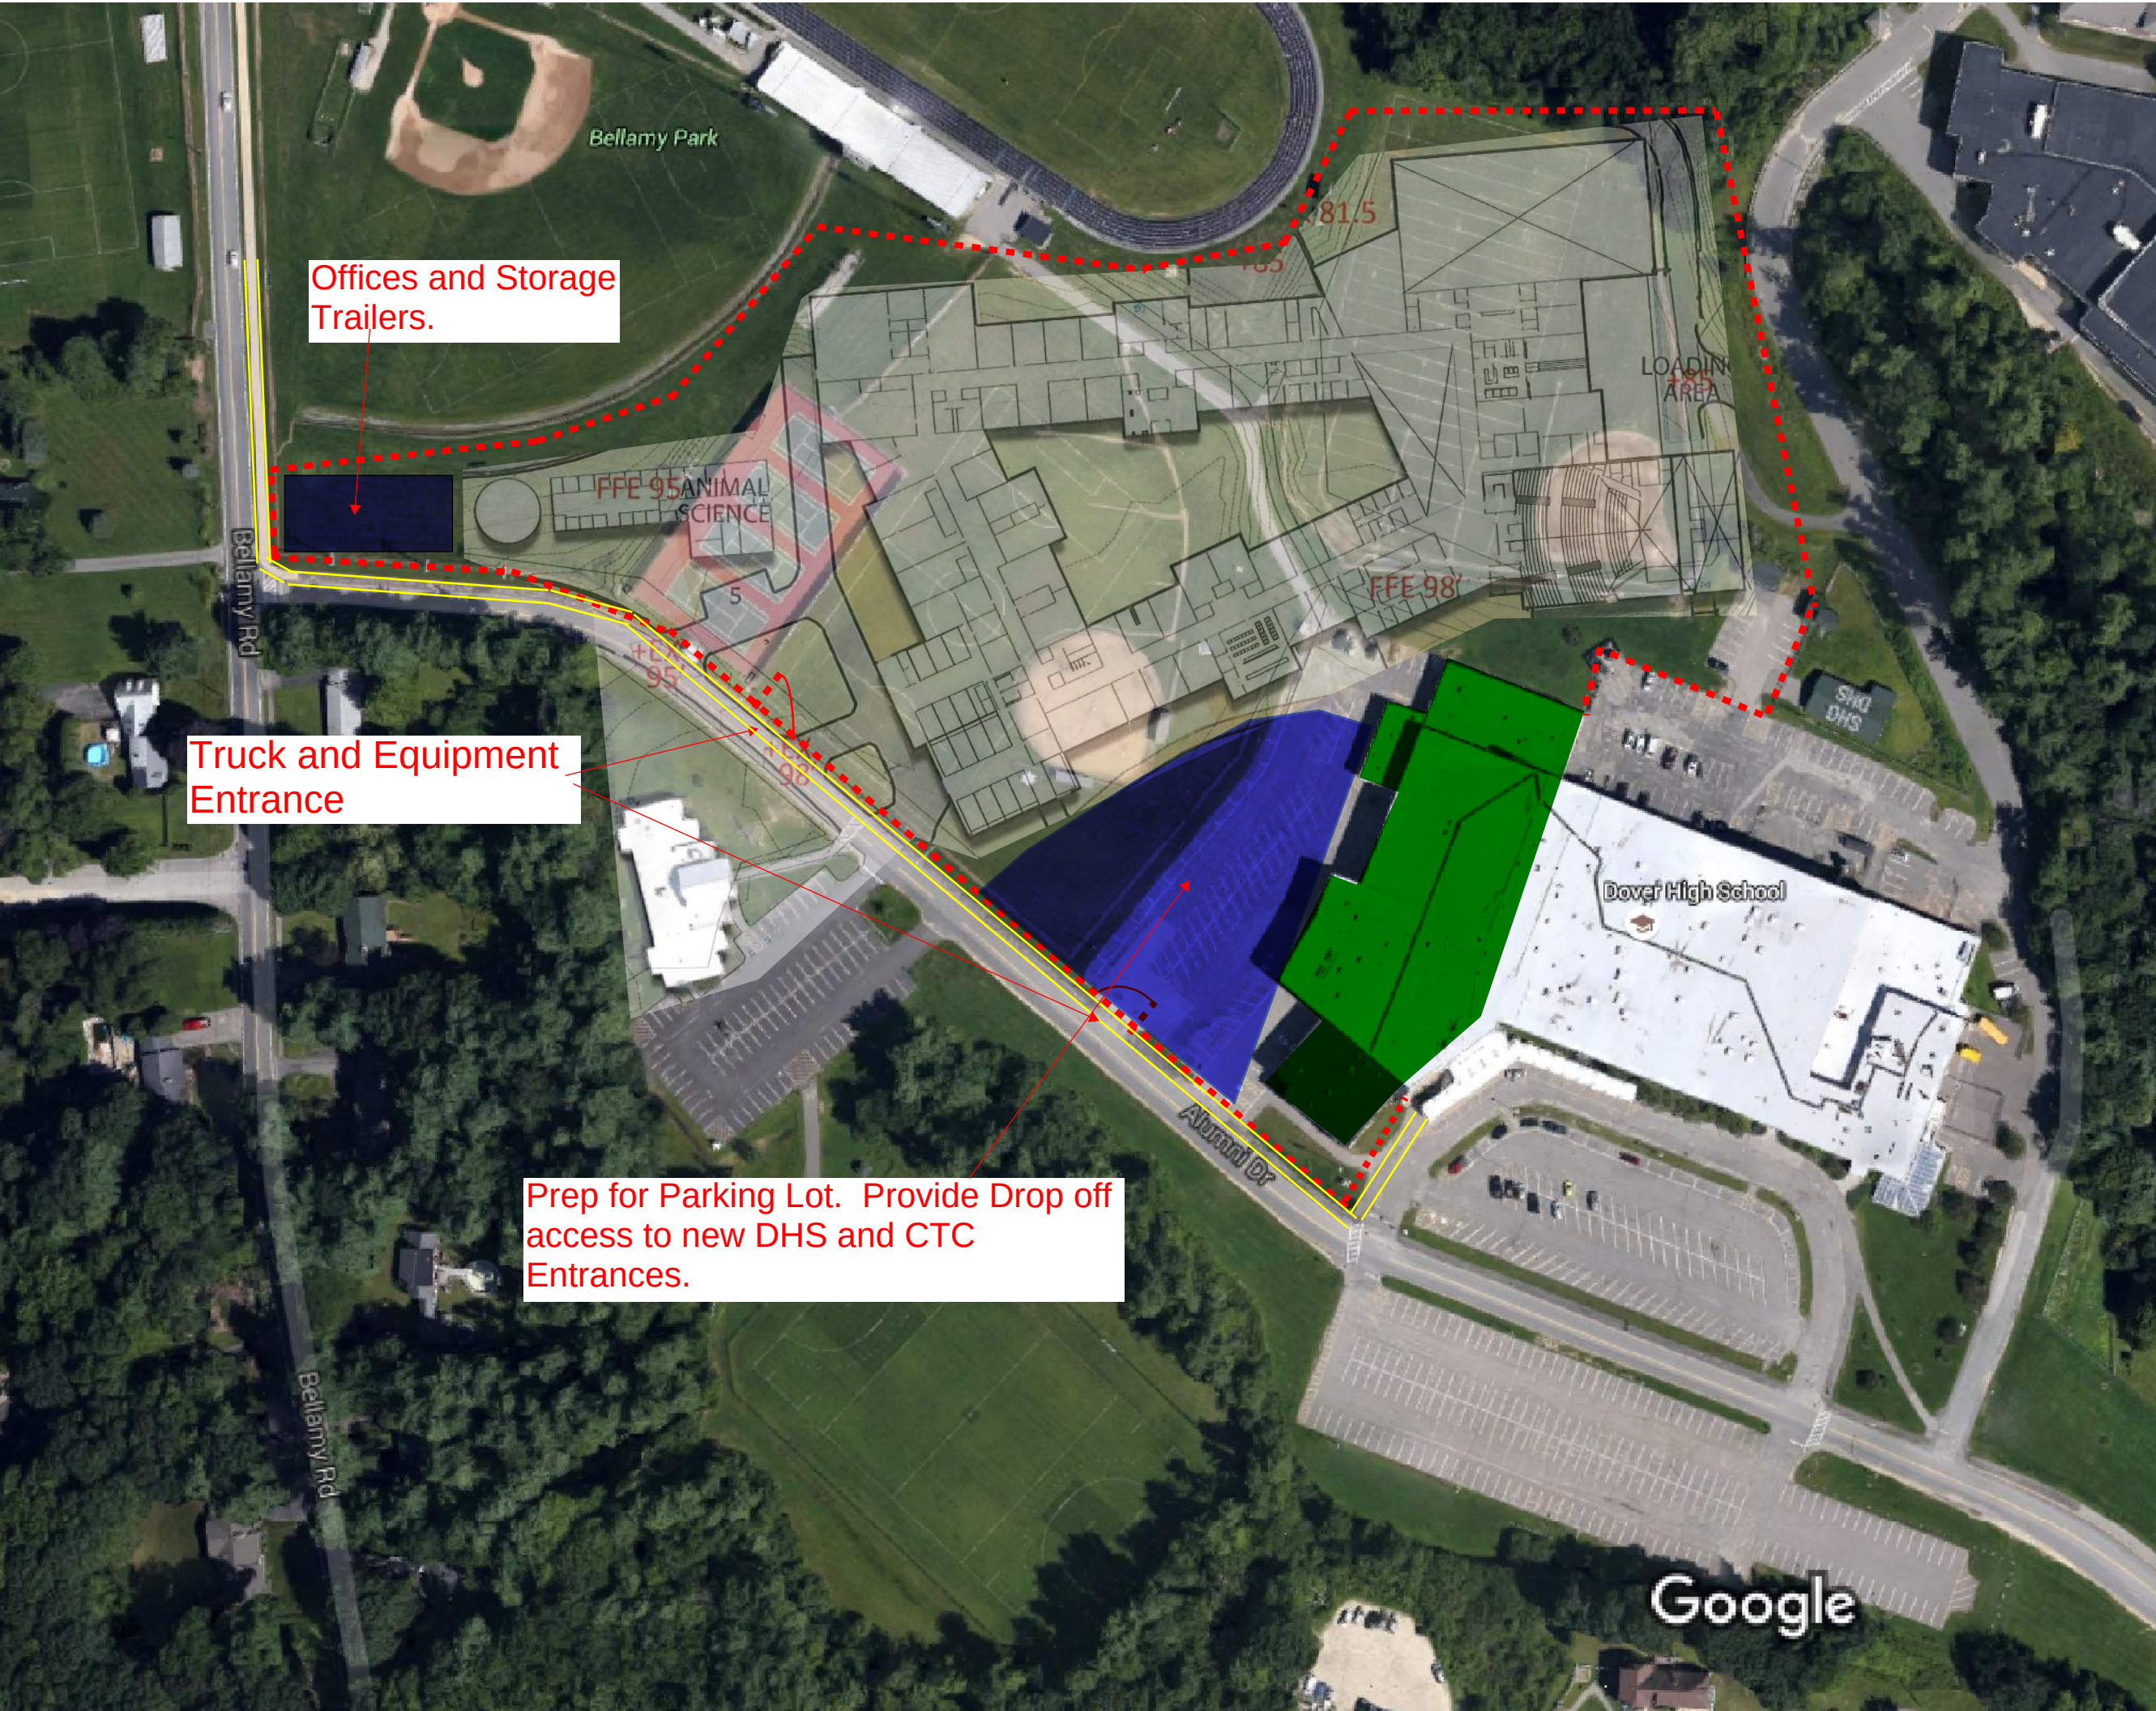


Offices and Storage Trailers.

Truck and Equipment Entrance

Prep for Parking Lot. Provide Drop off access to new DHS and CTC Entrances.

PHASE III:
June thru Aug, 2018
Abatement of existing Auditorium and Gymnasium.
Prep for Westerly Parking Lot.

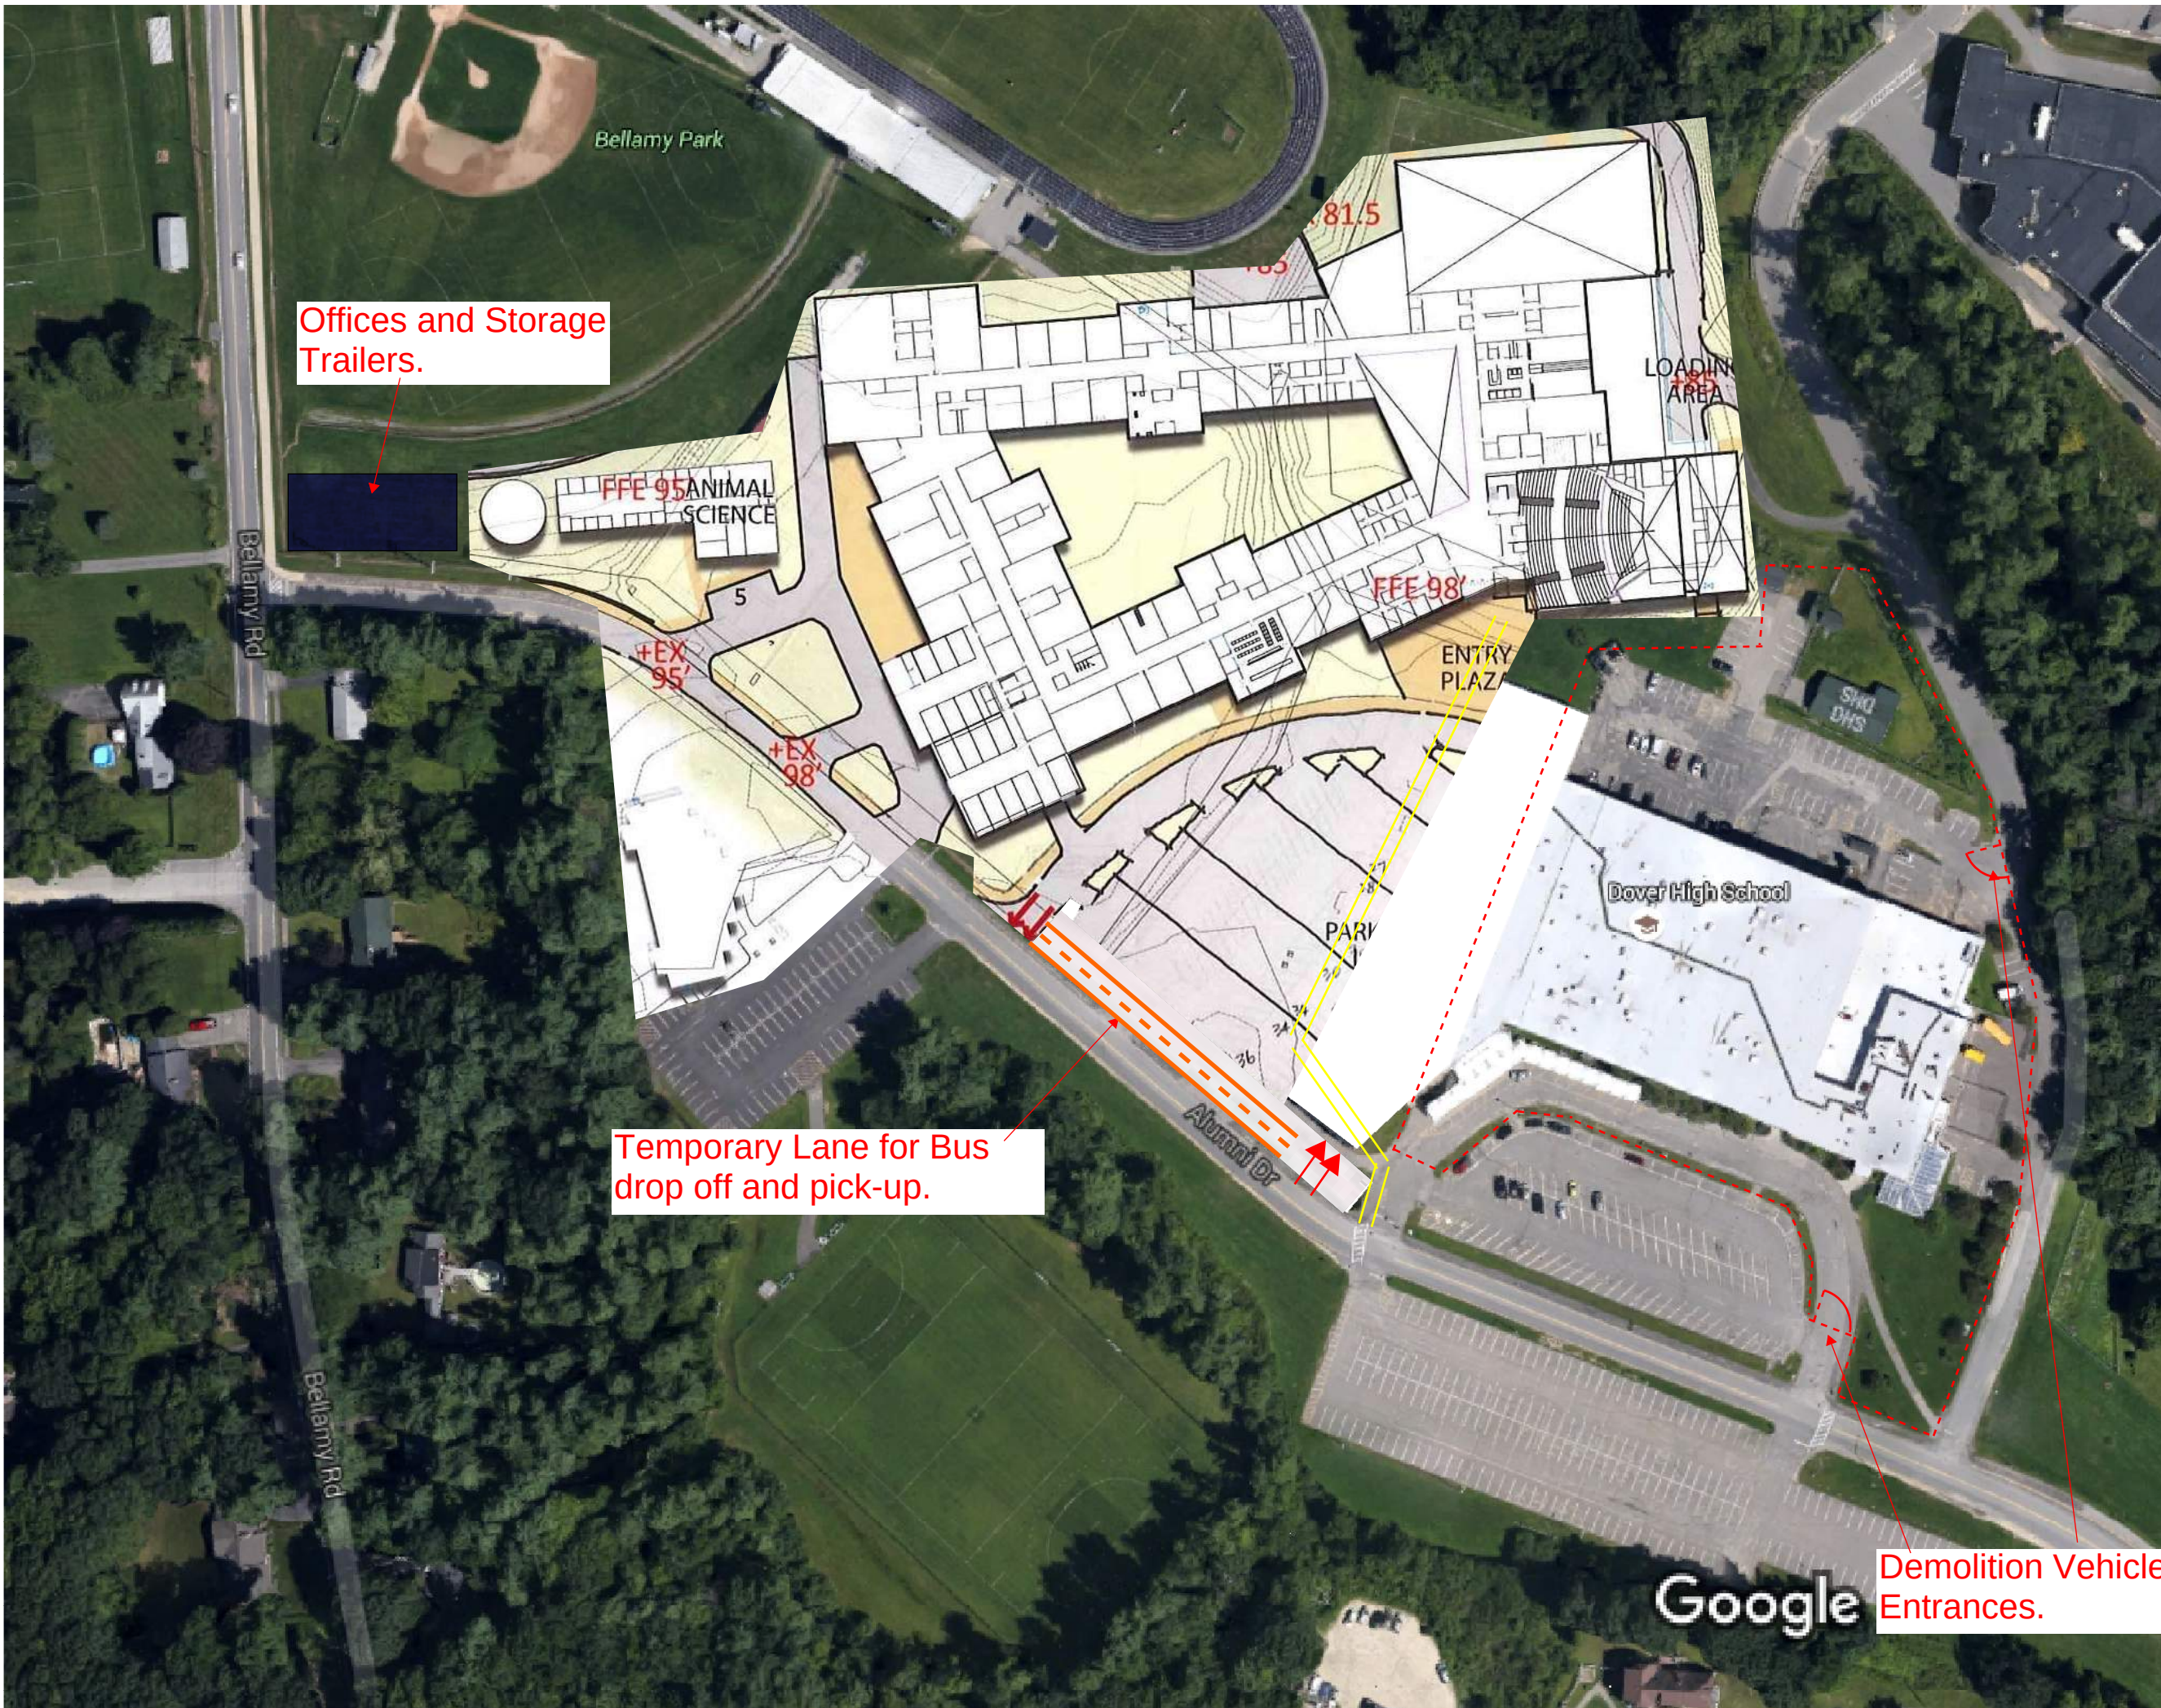


Offices and Storage Trailers.

Temporary Lane for Bus drop off and pick-up.

Demolition Vehicle Entrances.

PHASE IV:
Sept, 2018 thru March, 2019
Abatement and Demolition of
Existing High School and
CTC Structure.
Existing South Lots remain
in service during demolition.
Westerly portion of new lot
limited to staff parking and
pedestrian access to new
building. Final configuration
of completed lot to be
modified as construction
progresses.

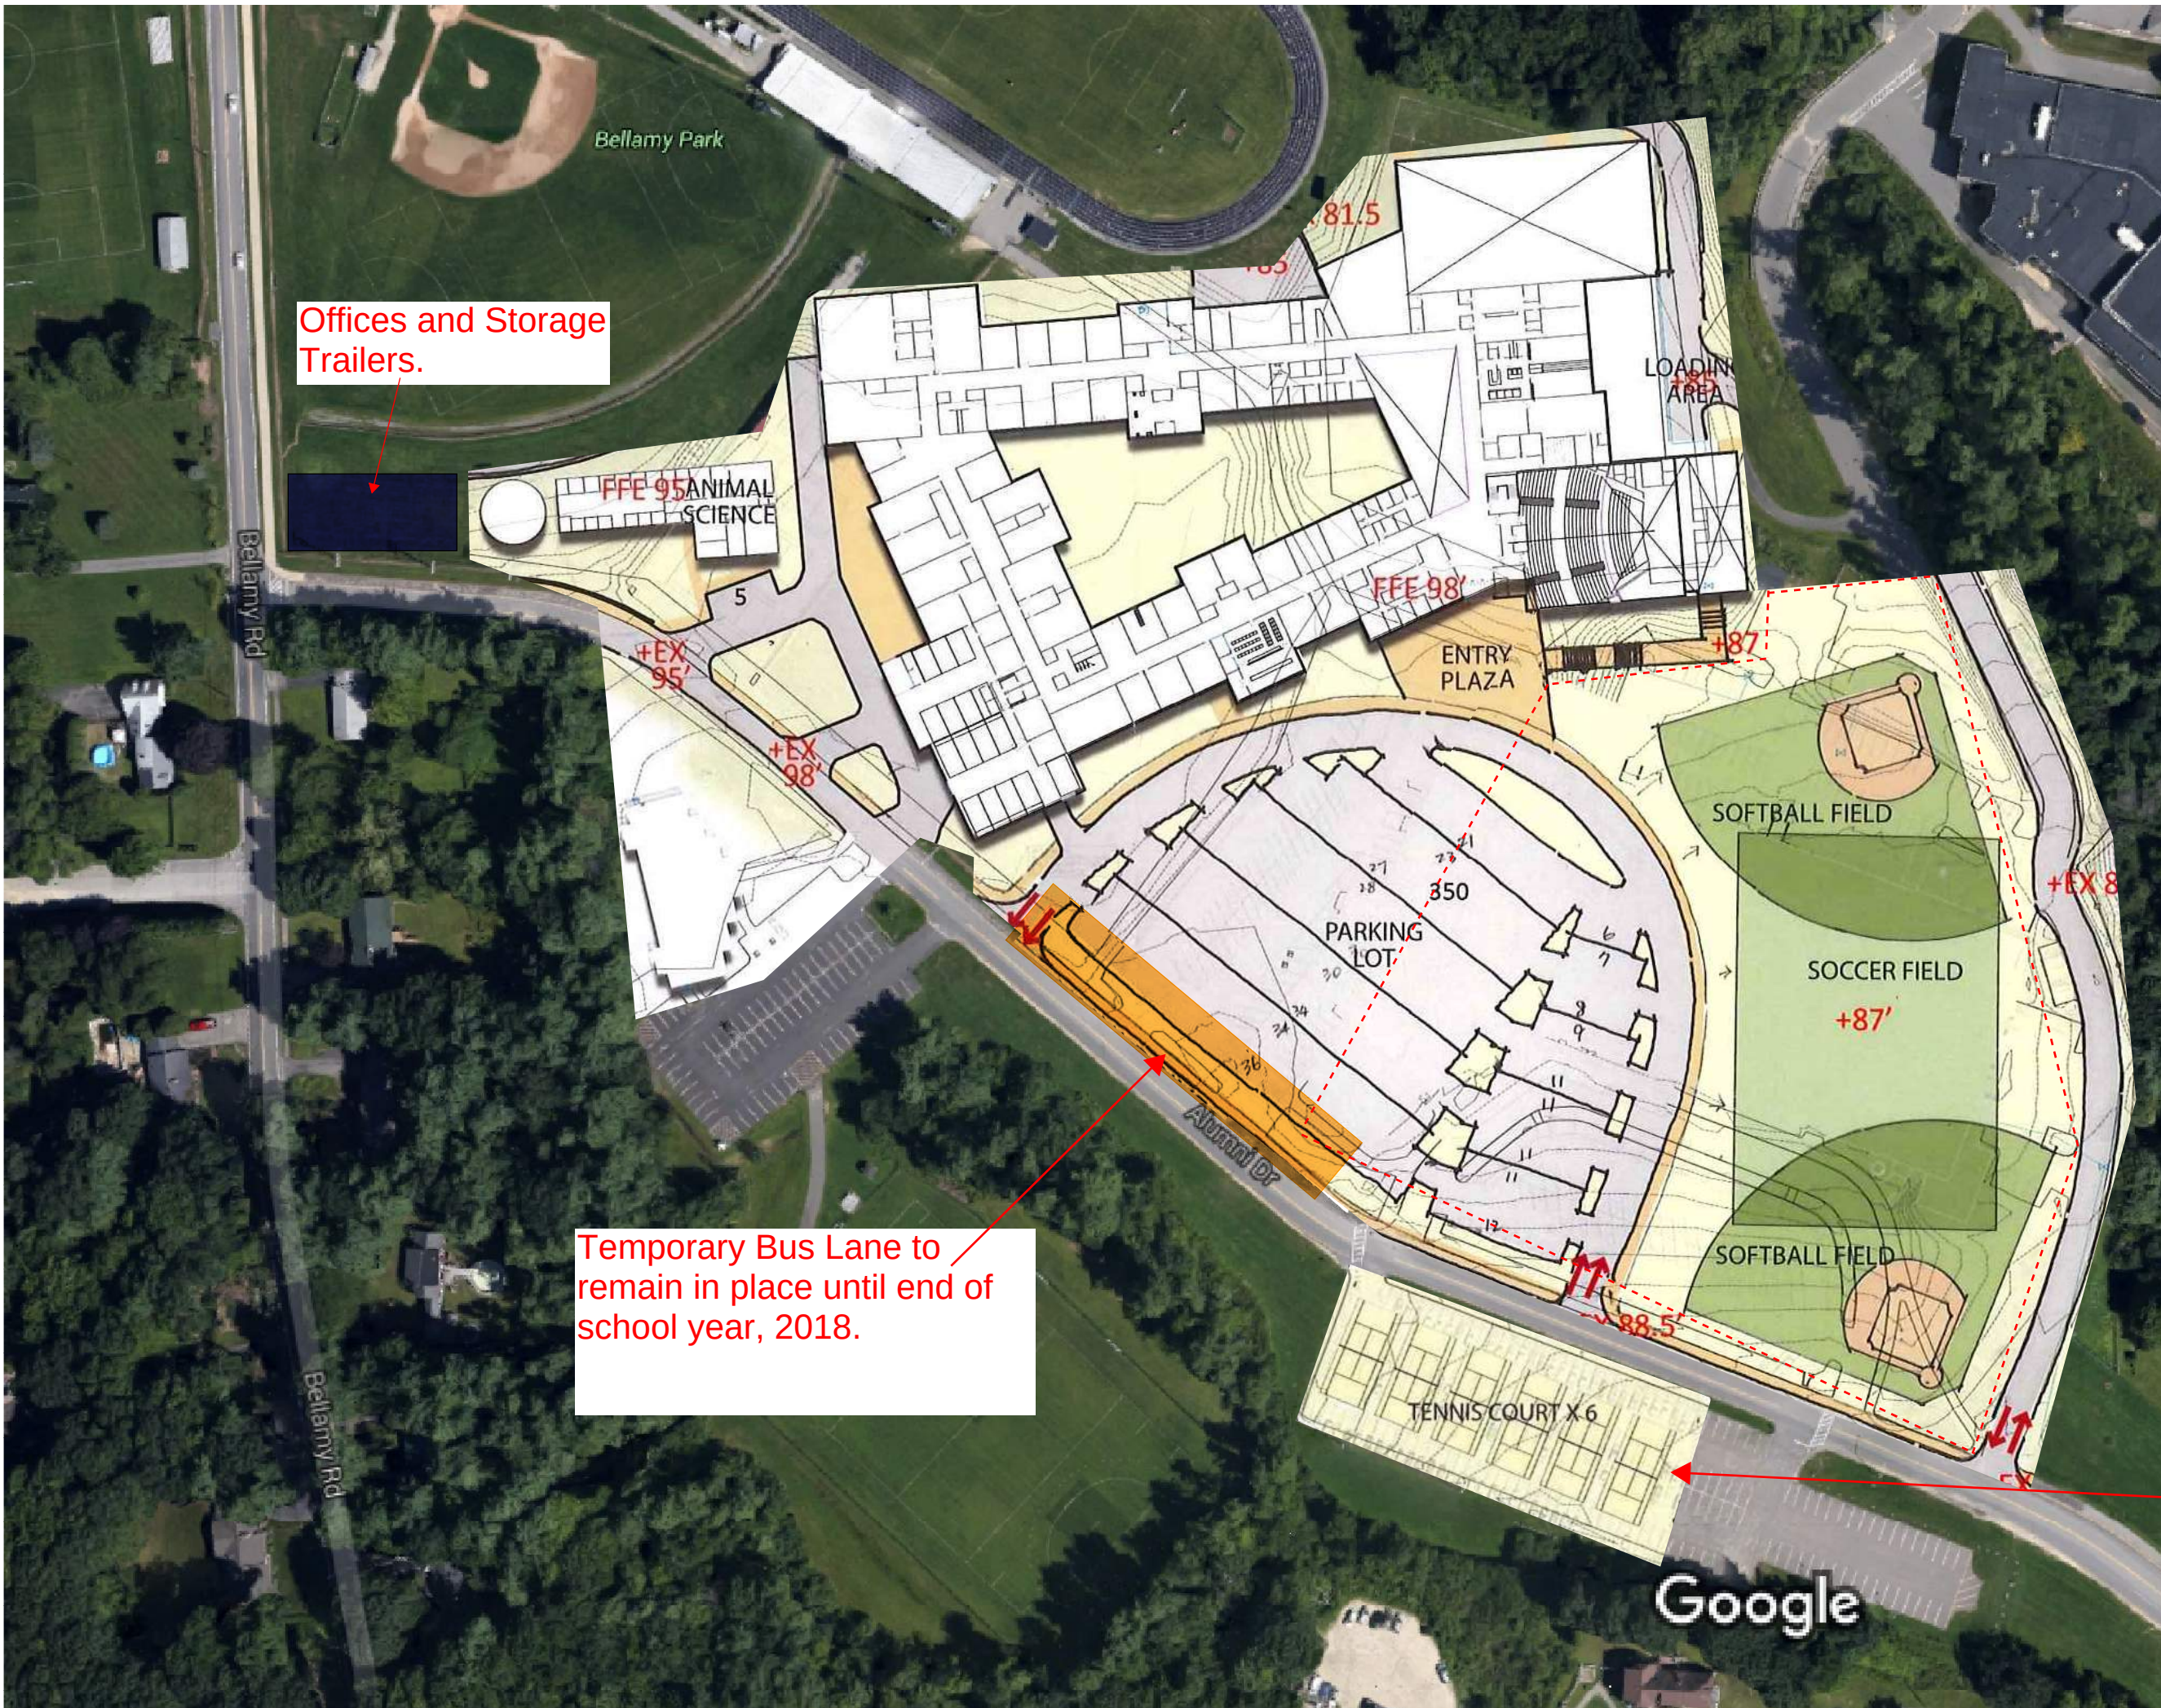

Offices and Storage Trailers.

Temporary Bus Lane to remain in place until end of school year, 2018.

PHASE V:
Apr, 2019 thru Aug, 2019
Construction of remaining section of new parking lot.
Construction of new softball and soccer fields.
Reconfiguration of roadways as necessary. Parking lot south of Alumni Drive would remain in service for duration of work.
Fields would not be available for Fall, 2019 sports.

PHASE VI:
New tennis court work to begin once new parking lot is complete on north side of Alumni Drive.
