




2014 Summer Operations – School Board Update
8/11/14

Summer 2014 Custodial Operations


Summer cleaning includes washing ceilings, lights, walls, windows and furniture. All furniture is removed from classrooms, floors stripped, (5) coats of finish applied, and furniture reset into classrooms. Status of each school as of 8/11/14 is as follows:

- **Woodman Park Elementary** **90% complete**
 - **Garrison Elementary** **90% complete**
 - **Horne Street School** **95% complete**
 - **Dover Middle School** **95% complete**
 - **Dover High School** **80% complete**
 - **Alternative School** **50% complete**
- **To date – 760 gallons of floor finish applied**


DOVER HIGH SCHOOL

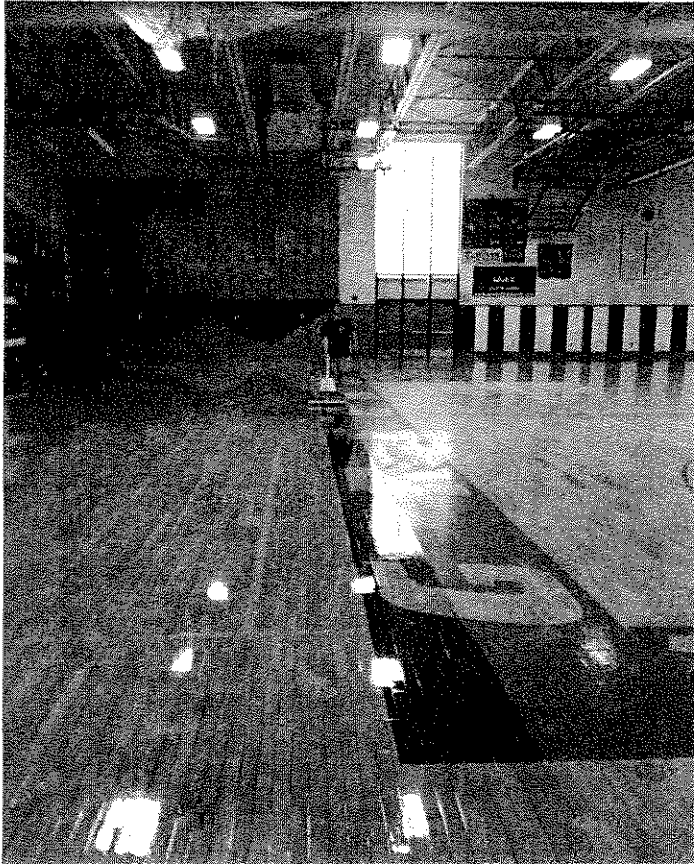


DOVER HIGH SCHOOL

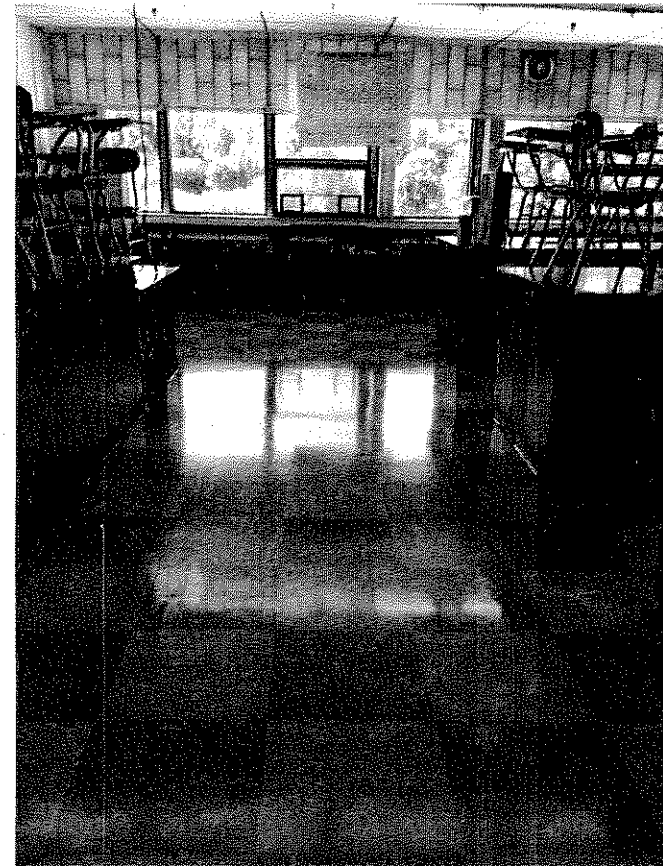



DOVER MIDDLE SCHOOL

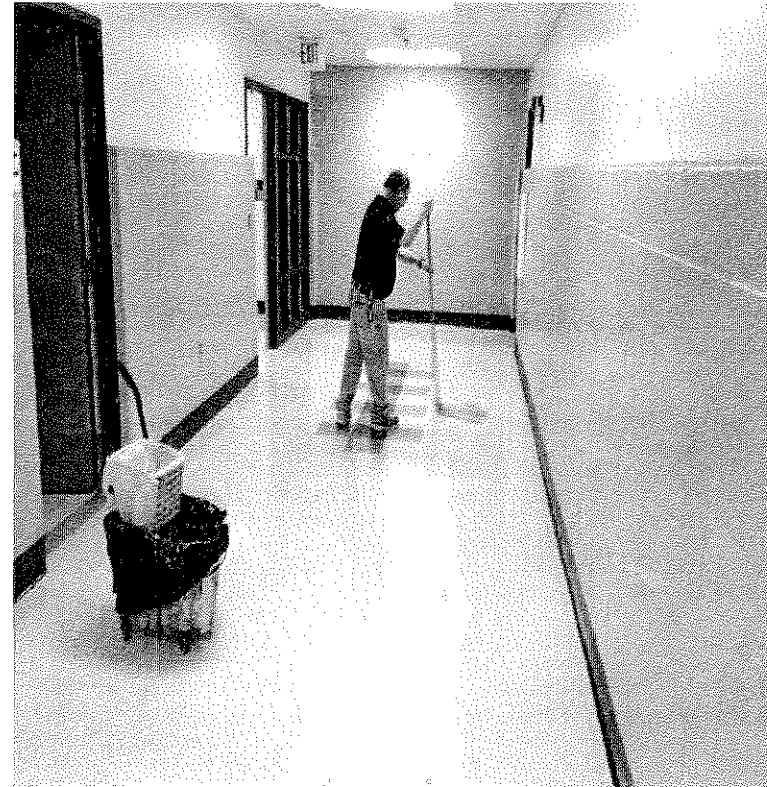



DOVER MIDDLE SCHOOL

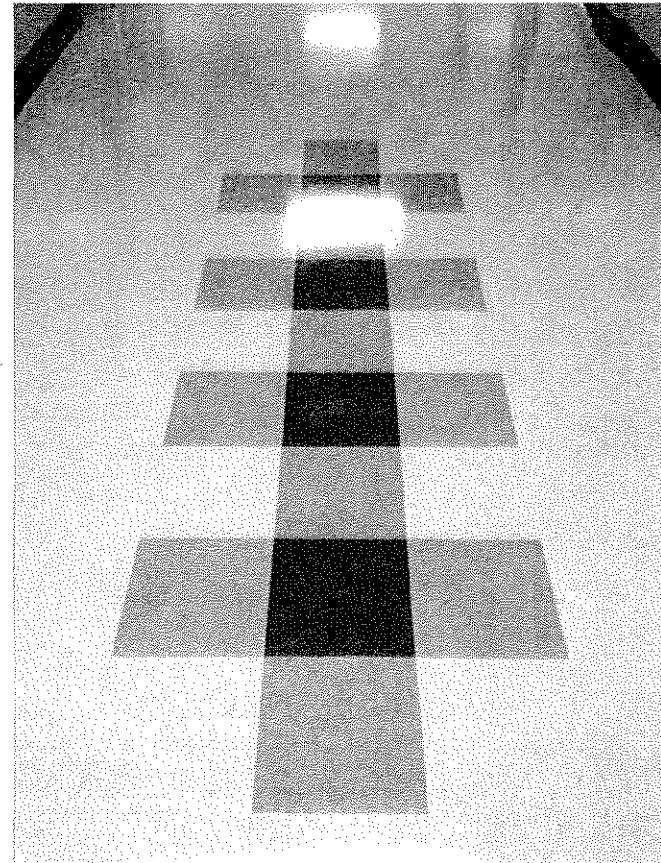



GARRISON ELEMENTARY

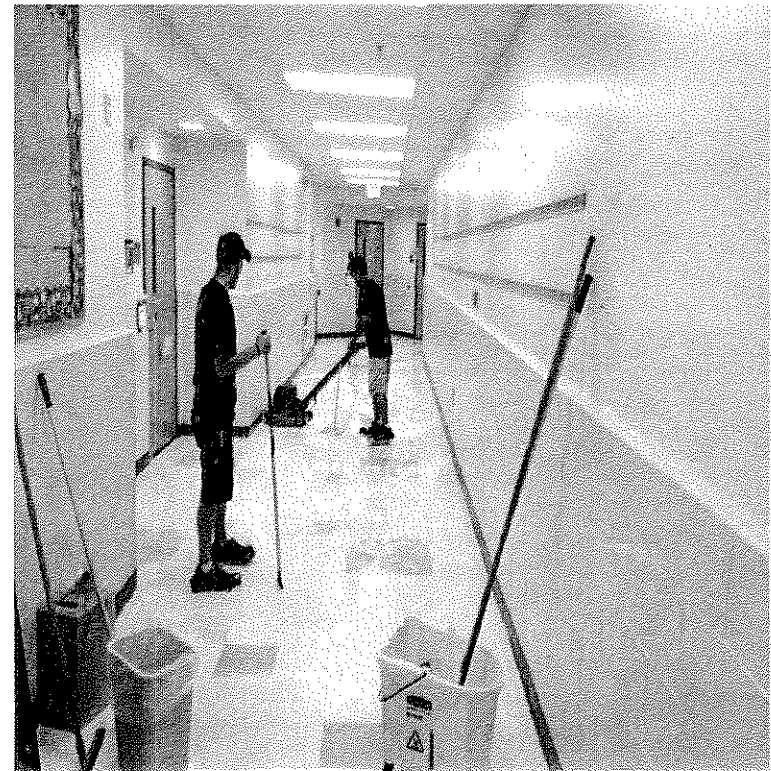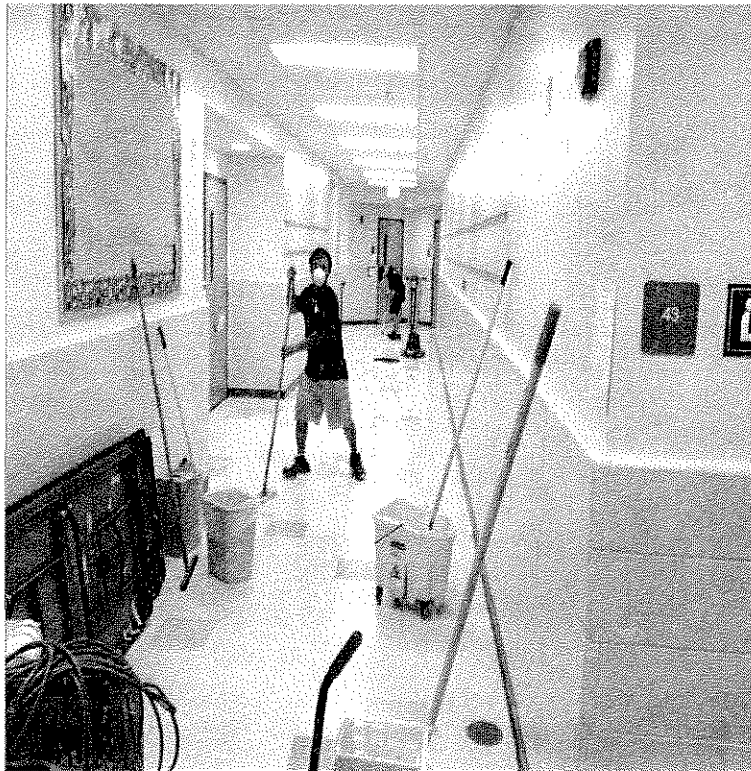


GARRISON ELEMENTARY

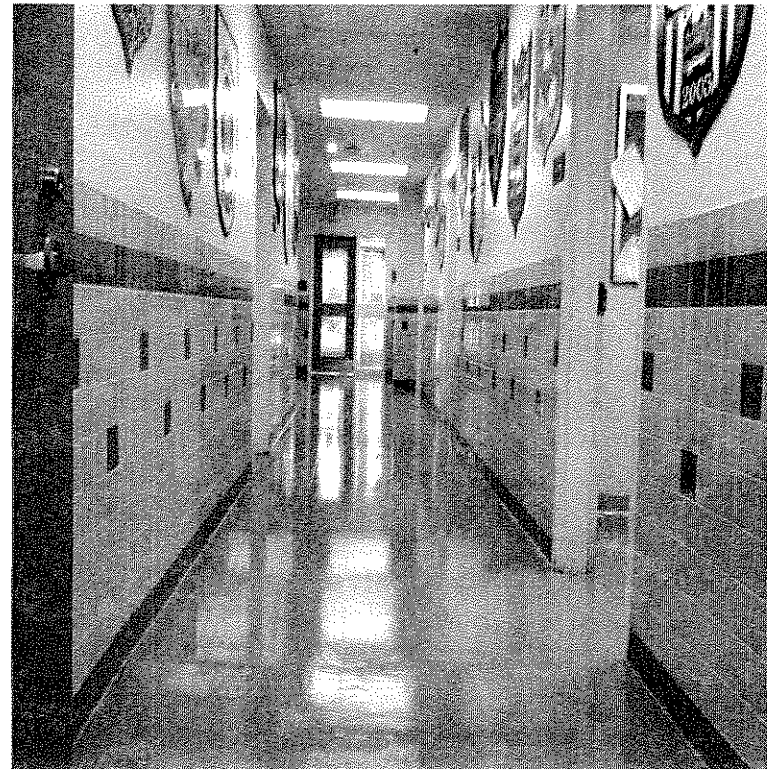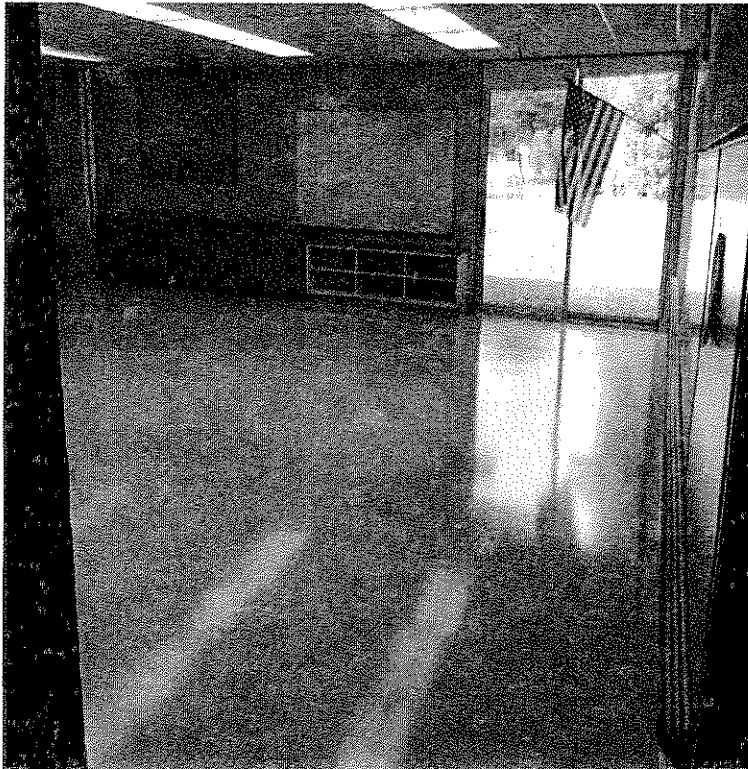



HORNE STREET SCHOOL

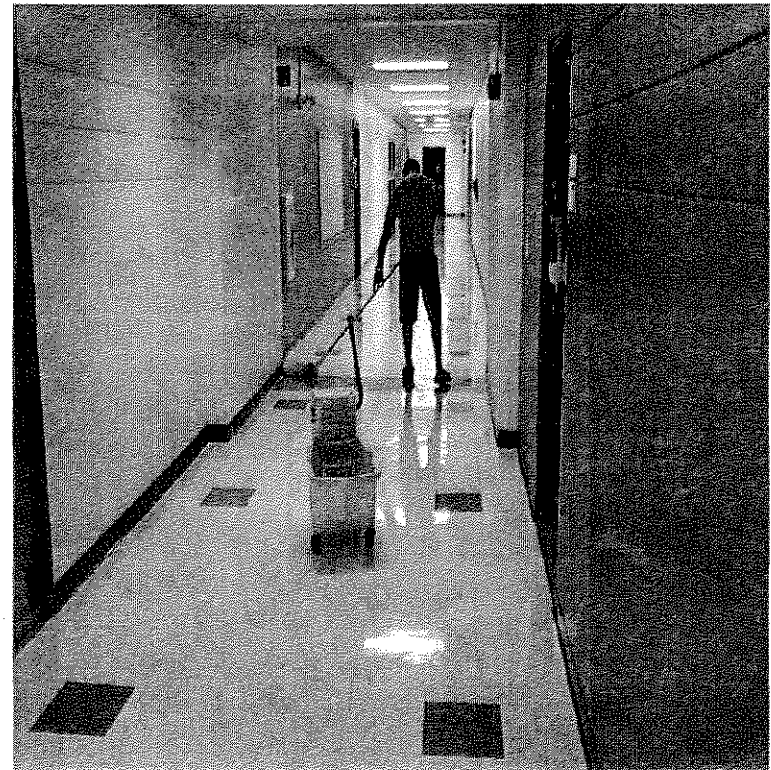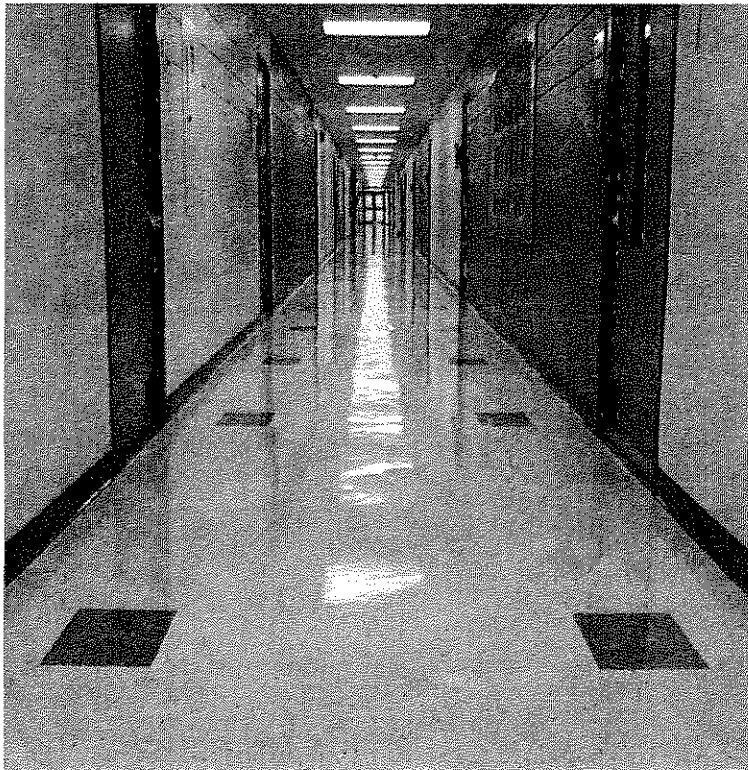



HORNE STREET SCHOOL

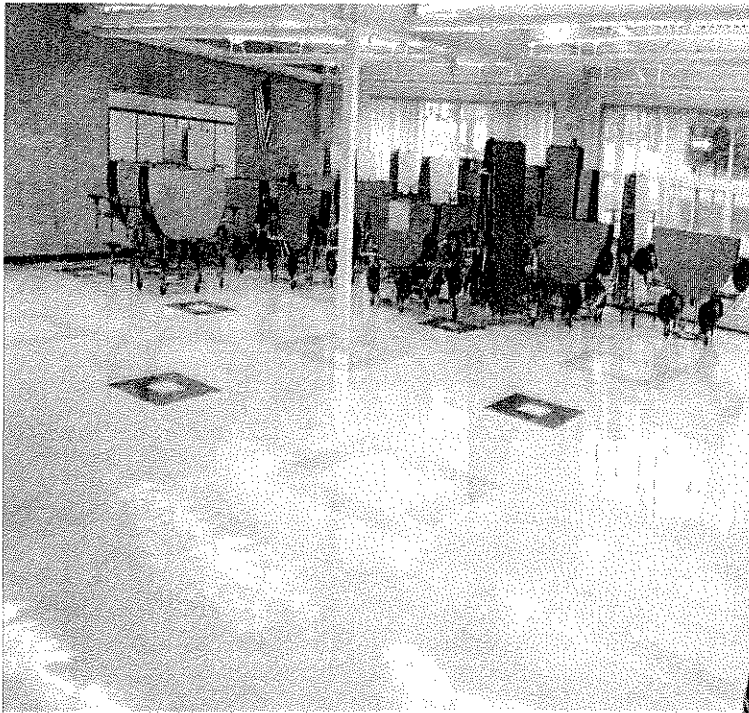

WOODMAN PARK SCHOOL

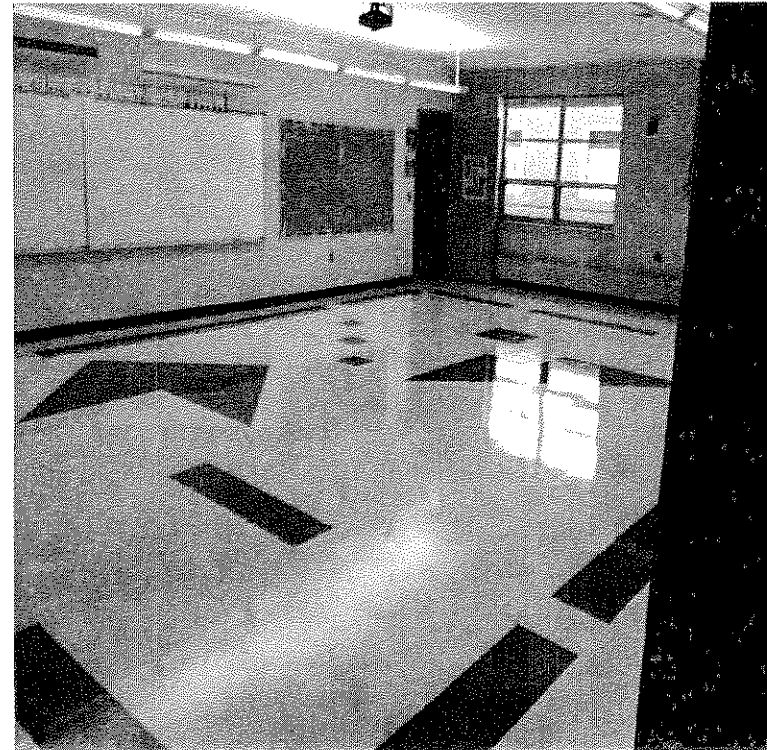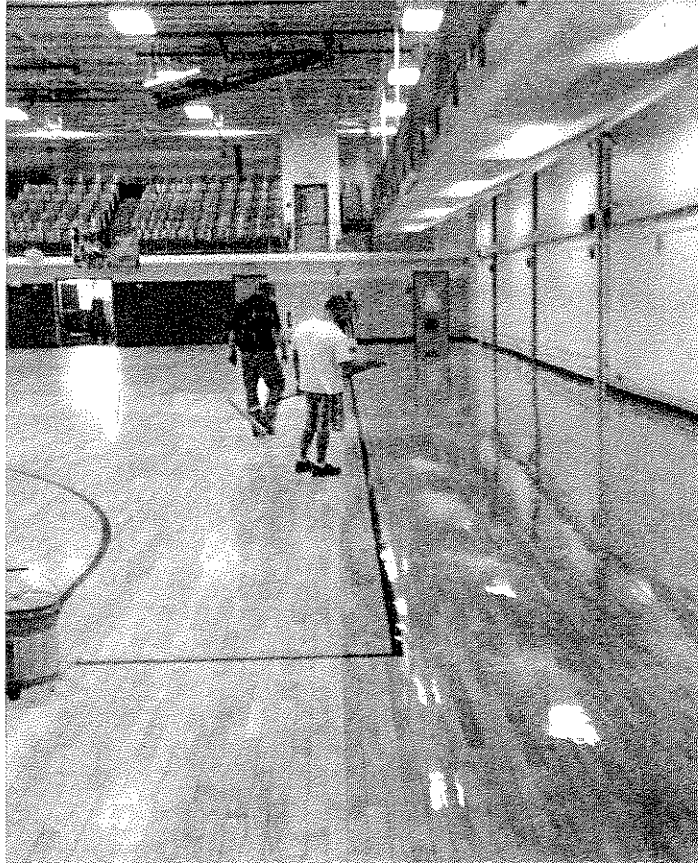



WOODMAN PARK SCHOOL

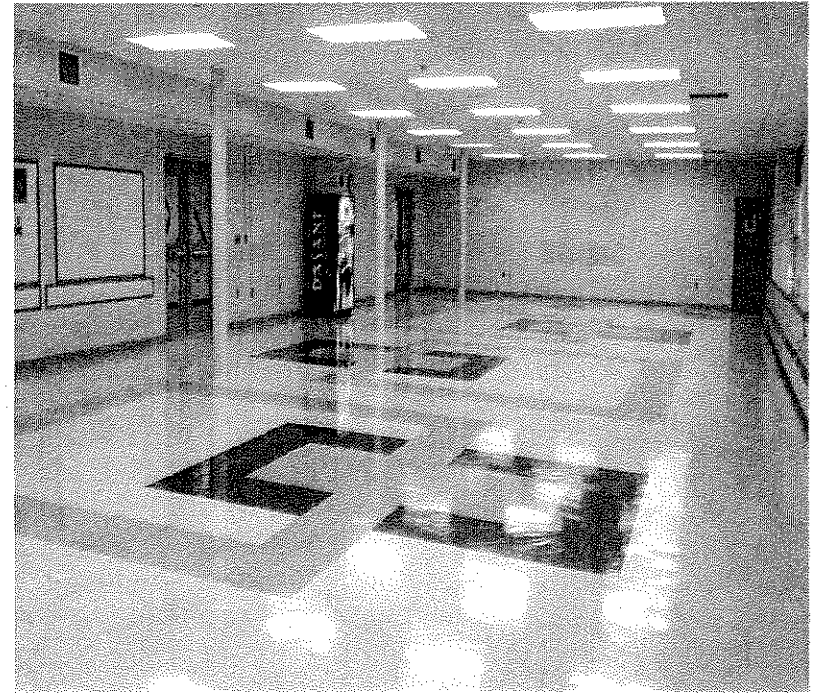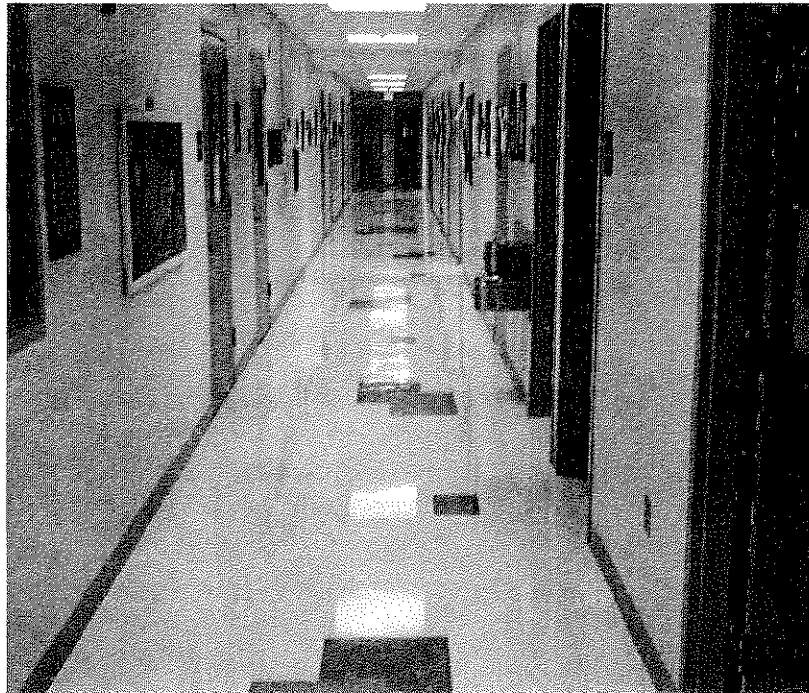



GROUNDS OPERATIONS

SEASON	FIELDS & GROUNDS INFORMATION	VENDOR	Completed	
SPRING	Rapid Dry product	DTZ	yes	
	Dry marking lime	DTZ	yes	
	Organic/synthetic blend fertilizer (Nature Safe)	Boston Company	yes	
	New infield mix put onto Varsity softball infield	DSD to supply/DTZ to spread	yes	
MARCH/APRIL	Spring start up on all fields	DTZ	yes	
APRIL	Fire Out Irrigation System & make repairs if needed	Hillside Landscaping	yes	
	Installing meters and back flow preventers (April)	By City	yes	
	Seed (blue/rye mix) upper softball outfield	DTZ	yes	
For April 1	Overseed wear areas (crowns and goals) (Late April)	DTZ	yes	
	Order Pot-O-Potties (cleaned Tuesday & Friday)	1 hndcp and 1 regular on Bellamy	yes	
		1 hndcp and 2 regular on Dunaway football	yes	
		1 hndcp on Fisk Field	yes	
	Turn water on	Once threat of freeze is over	yes	
LATE SPRING/EARLY SUMMER	Spray fence lines with weed control	Bio Spray	yes	
	Acelepryn grub preventer in place of Merit	Boston Company	yes	
	Slice seed all athletic fields/Aerate all fields	Boston Company	yes	
	500 lbs of 50/50 seed Blue/rye blend	DTZ	yes	
	Aerate all athletic fields	Boston Company	yes	
SUMMER	Cut back growth on fence lines	DTZ	yes	
	August	Spray fence lines with weed control	Bio-Spray	yes
		Broadleaf application on all fields		
		Repair goal mouths on Fisk Field	Boston Company / New England Pro Turf	yes
FALL	350 lbs overseed football fields and goal mouths	DTZ	Throughout Sept.	
	Fertilizer	Boston Company		
	Pallets of pelletized lime	DTZ		
	Blow Out Irrigation System for winter	Hillside Landscaping		
	Turn H2O off	After Thanksgiving Football game is over.		
	Have Port-O-Potties seasonally treated and billing stop	Dave's		
GENERAL	Mowing heights vary according to field usage			

ATHLETIC FIELDS

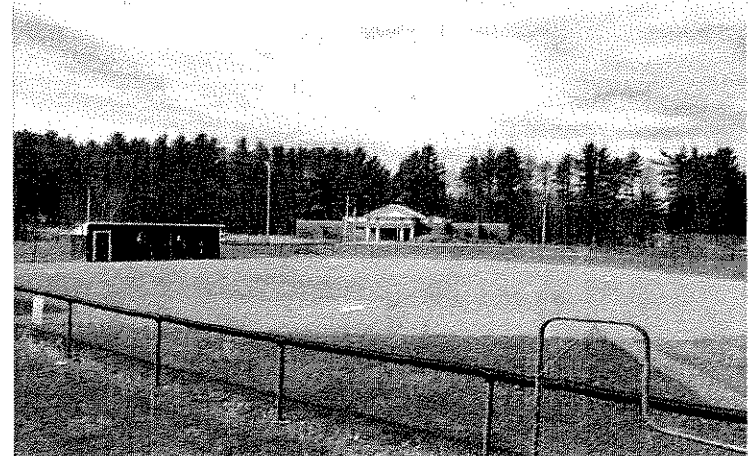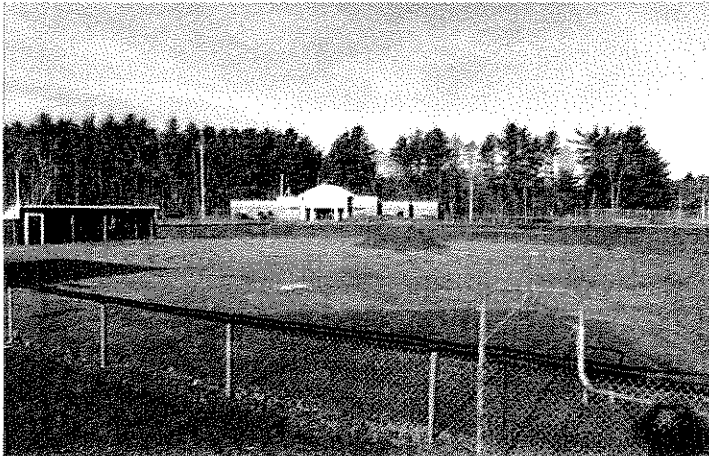

ATHLETIC FIELDS

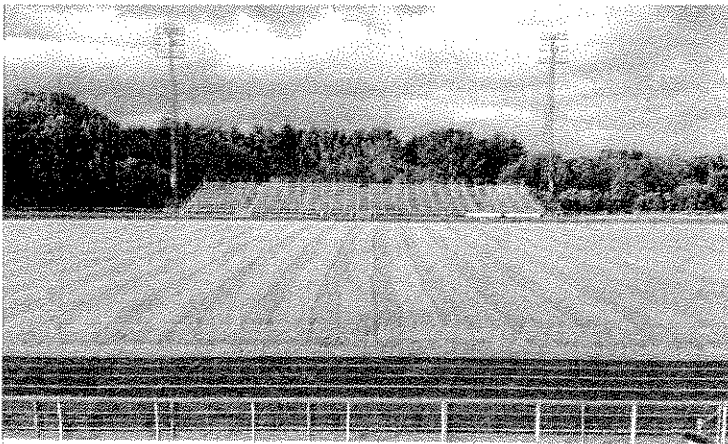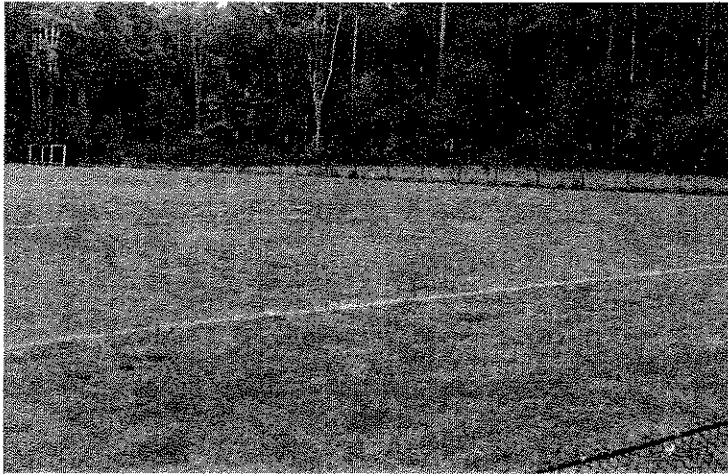





SUMMER PROJECTS

SCHOOL	PROJECT DESCRIPTION	VENDOR	PO #	COST	STATUS
DHS	Replace one bank of bleacher seats	Hussey Seating	201413043	\$10,525.00	scheduled 9/19 & 9/22
DMS	VCT work in wing rooms (4)	Tri-City Flooring	201412995	\$1,959.00	Completed 8/8/14
DMS	Repair fencing around dumpsters	AAA Fence	201413039	\$2,680.00	Completed 8/6/14
DMS	Replacement seats in Renaissance	Hussey Seating	201413042	\$3,334.00	seats on order, Facilities will install
GES	Window screens	All Door and Lock	201412994	\$1,904.00	screens made, facilities to install
GES	Window tinting	Visions	201413044	\$3,475.00	60% complete will be completed week of 8/11
GES	Asbestos Abatement	RPF	201413040	\$600.00	scheduled for week of 8/11
GES	Wallpaper / Paint 3 rooms	Ray Talon Painting	201500624	\$3,300.00	completed, facilities installed new cove base & painted door trim
DSD	Pavement repairs	Tri State Paving	201413041	\$36,344.00	in progress
DSD	Power for projectors	undecided			collecting proposals
DMS	Walk-in Cooler floor repair	undecided			collecting proposals
Total				\$64,121.00	
WPS	Vinyl floor replacement in staff bathrooms	Hogan	Facilities	\$5,000.00	in progress
DSD	Painting 20+ rooms	DTZ			in progress
DSD	Life safety inspections	Norris / SSI			in progress
DSD	100+ work orders	Facilities			in progress
DSD	Emergency power/lighting tests	Facilities			in progress




DMS VCT Tile repair

DMS Fence repair

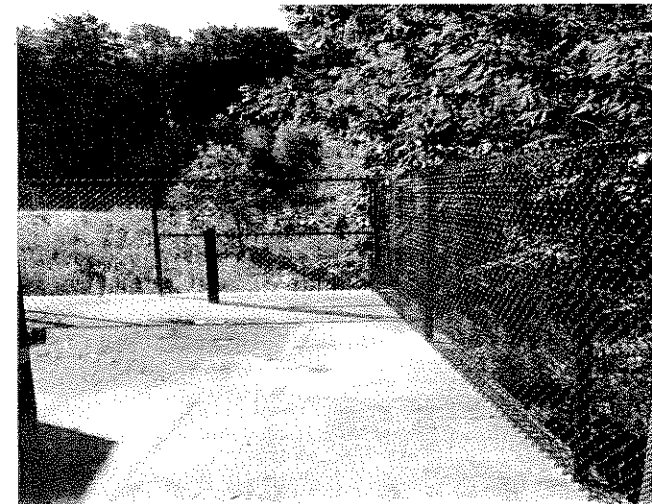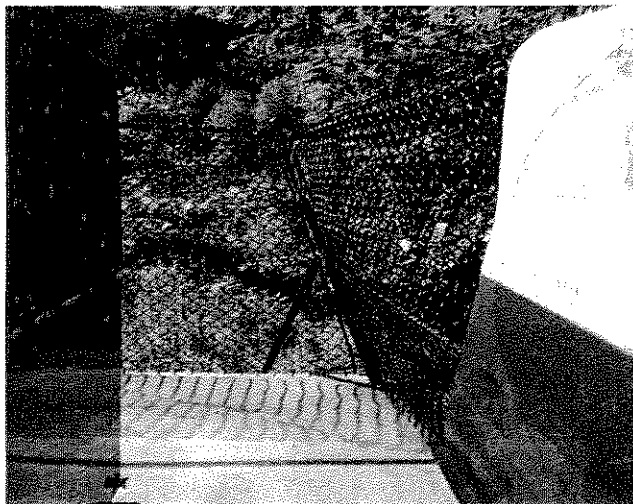

GES Wallpaper removal

DHS Pavement repair

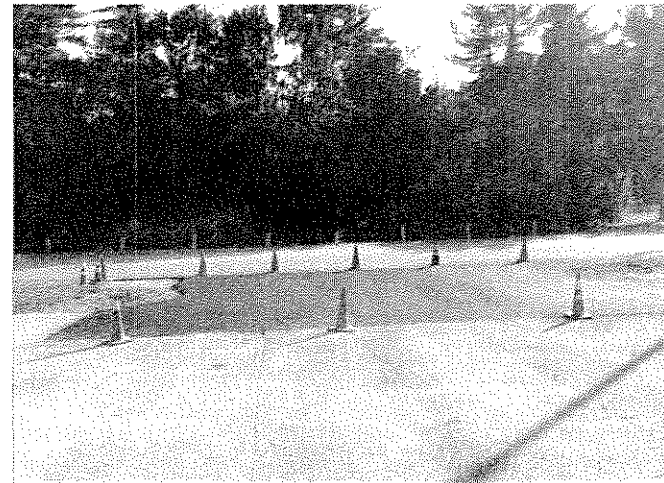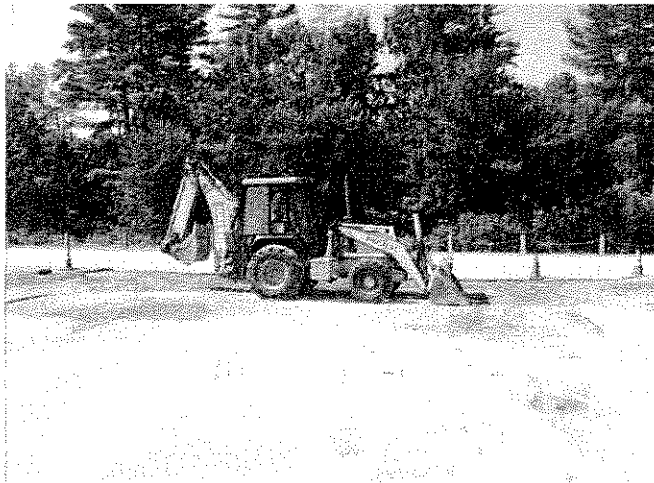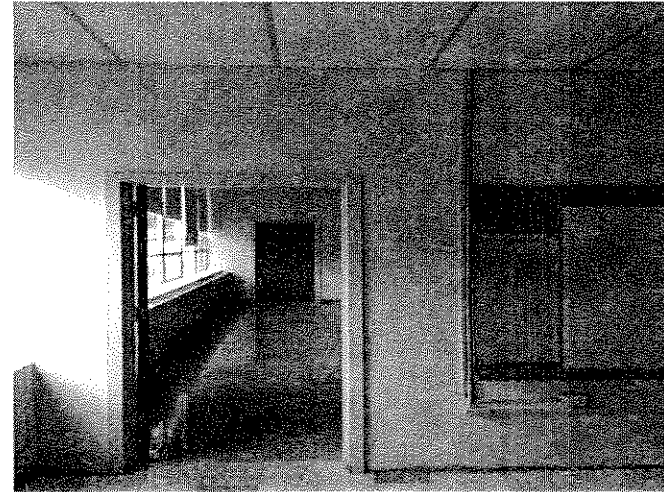

WPES floor replacement District Painting projects

